


Fuller Middle School



May Progress Updates

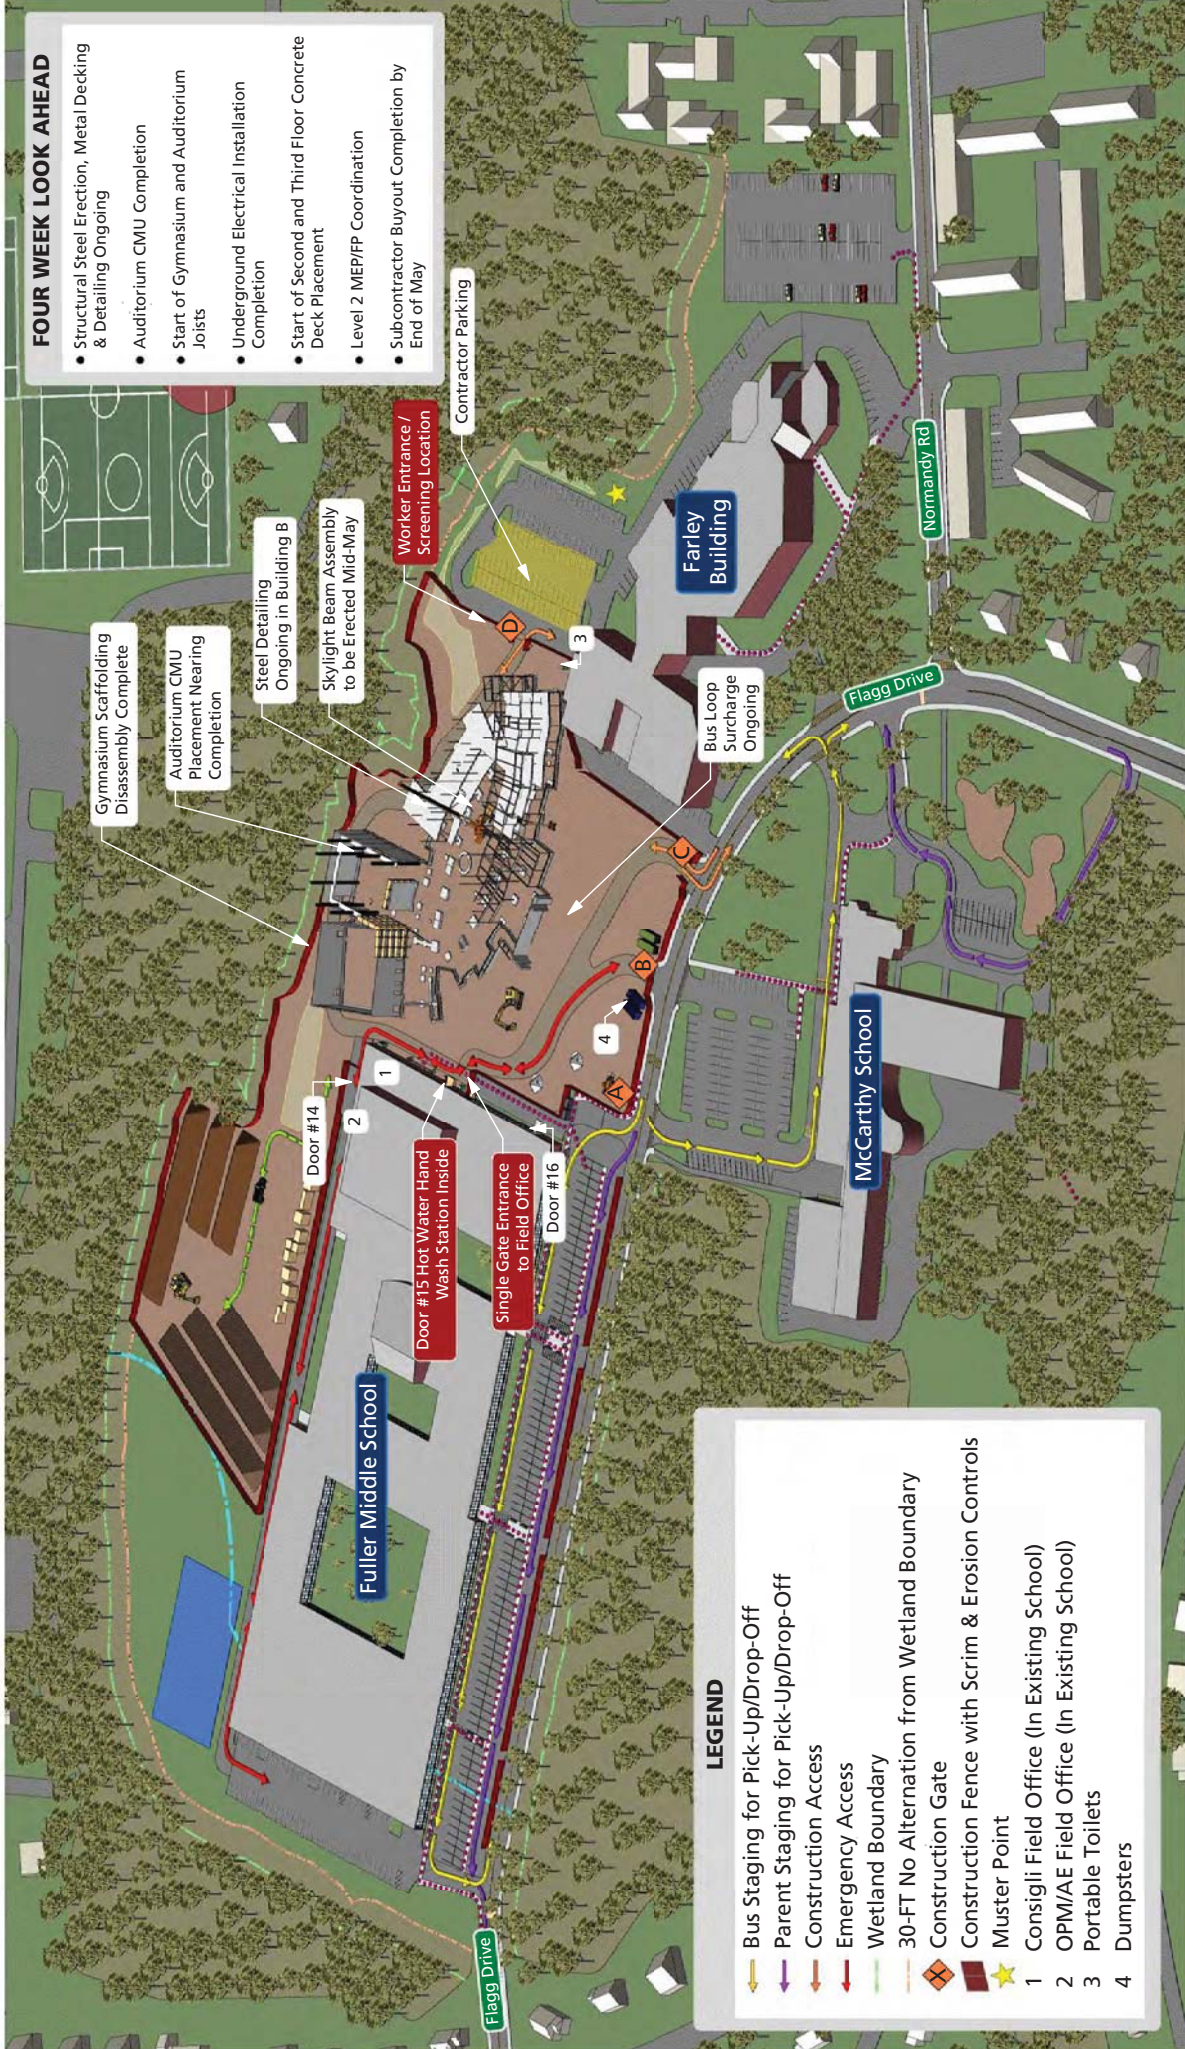

- ### FOUR WEEK LOOK AHEAD
- Structural Steel Erection, Metal Decking & Detailing Ongoing
 - Auditorium CMU Completion
 - Start of Gymnasium and Auditorium Joists
 - Underground Electrical Installation Completion
 - Start of Second and Third Floor Concrete Deck Placement
 - Level 2 MEP/FP Coordination
 - Subcontractor Buyout Completion by End of May

LEGEND

- Bus Staging for Pick-Up/Drop-Off
- Parent Staging for Pick-Up/Drop-Off
- Construction Access
- Emergency Access
- Wetland Boundary
- 30-FT No Alteration from Wetland Boundary
- Construction Gate
- Construction Fence with Scrim & Erosion Controls
- Muster Point
- 1 Consigli Field Office (In Existing School)
- 2 OPM/AE Field Office (In Existing School)
- 3 Portable Toilets
- 4 Dumpsters

Fuller Middle School

Executive Summary

Project Overview

Gym and Auditorium Roof Joists have now been set and steel erection in Building Area C has begun. Mechanical coordination has been substantially completed for Level 2. Level 1 is now the final building area to be coordinated.

Steel erection began on 3/16 with approximately 1/2 of the steel for the project erected through the end of May. Currently the majority of "B and D Building" (the eastern half of the classroom wing, and Gym/Auditorium) has been erected and decked, with steel detailing and concrete deck pours ongoing.

Consigli has maintained the protocols related to the threat of COVID-19 and subcontractor compliance on the project has been excellent. These include onsite cleaning stations, elimination of all non-essential meetings in person, and redundancy contingencies to allow for continuous project supervision. Consigli is staying in constant communication with our subcontractor partners to evaluate any material or manpower impacts and presents all current delays at the weekly OAC meeting. Consigli has been proactive in seeking opportunities to mitigate schedule impact. Schedule impact to steel fabrication will be finalized upon completion of erection onsite.

Final buyout savings for the project totals \$830,424.

Financial Status

Change Order #10 was presented at the SBC meeting on May 11th, 2020 in the amount of \$145,565.02. This change order brings the new contract amount to \$77,706,683.80.

Quality Update

Overall quality to date has been good. Structural Steel submittal review is nearing completion and MEP submittal review is ongoing. Weekly coordination meetings, with Architect involvement, are ongoing to mitigate any MEP clashes in the field before they occur. Testing is ongoing for soil compaction, mortar/grout strength and steel connections.

Safety continues to be excellent; Through May, we have 347 days onsite without a lost time incident.

Roadblocks

There are no roadblocks currently open.


Schedule Milestones

Completion of Auditorium CMU - 05/08

Placement of SOD Building Area B 2nd Floor - 05/21



Photos 1 & 2: Aerial Drone Views of the site showing the building superstructure construction in progress.

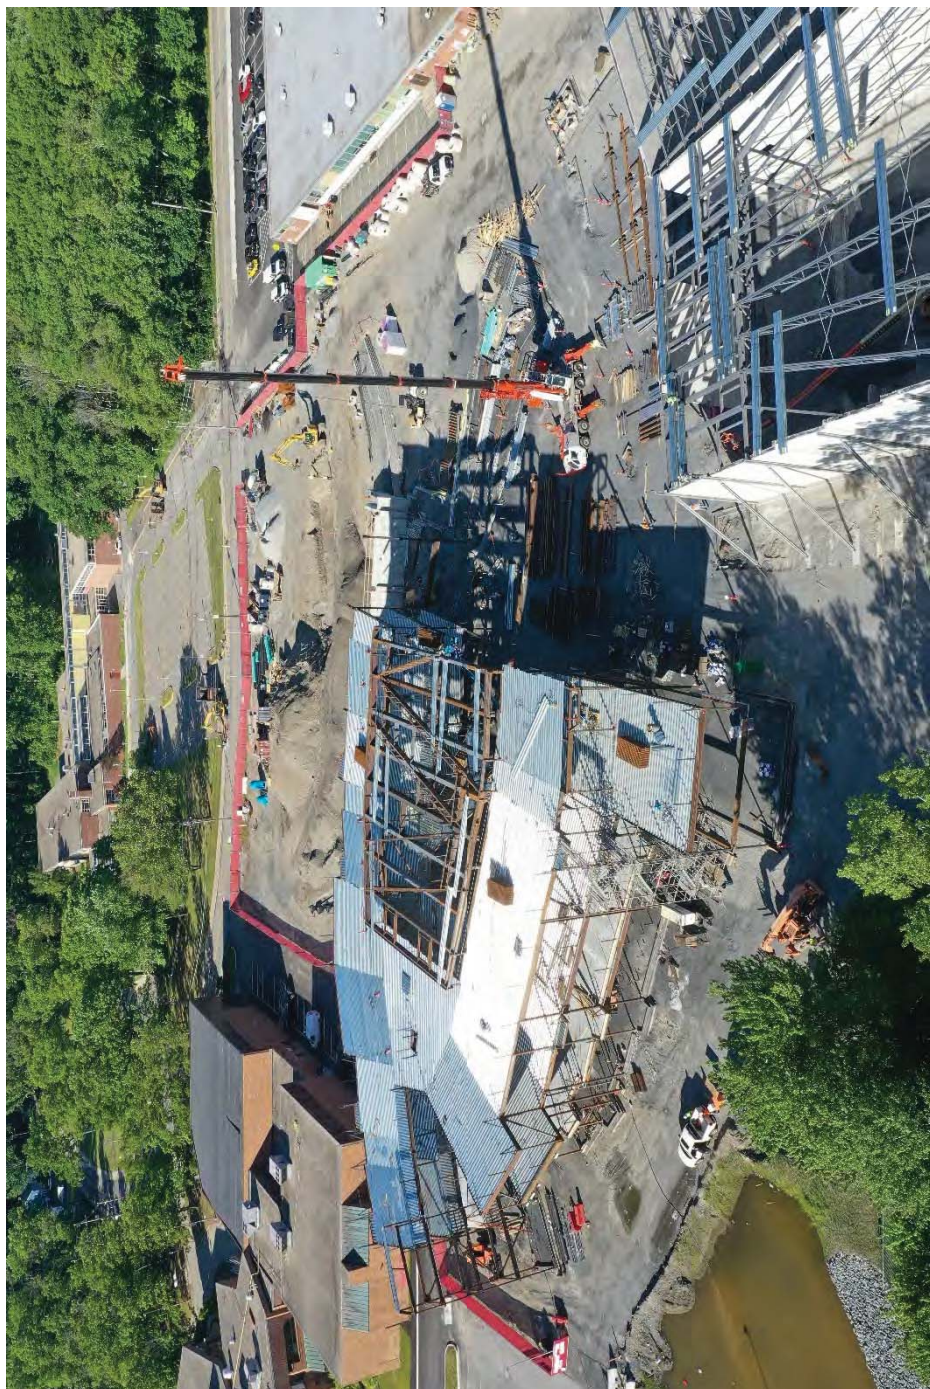

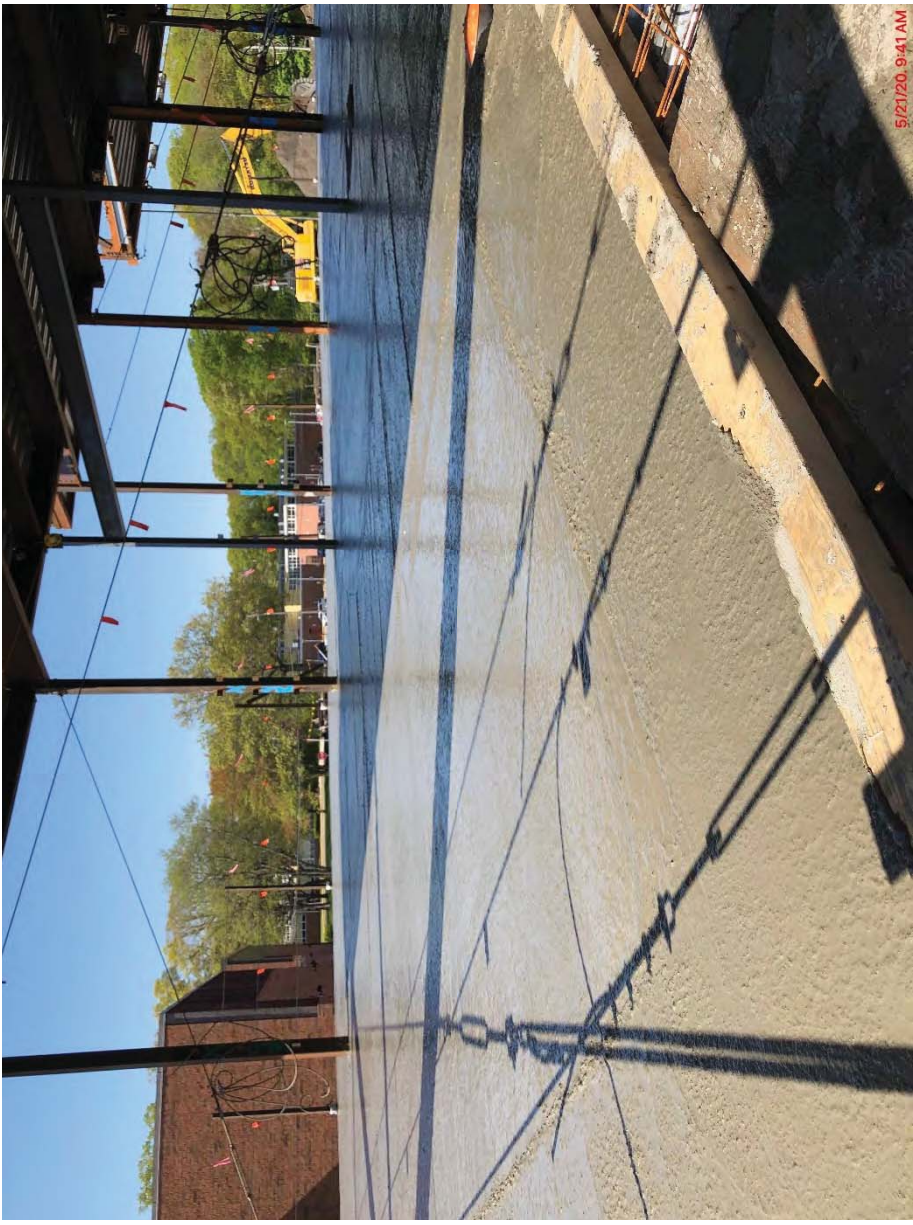


Photo 3: First Slab on Deck placed at Building B Second Floor

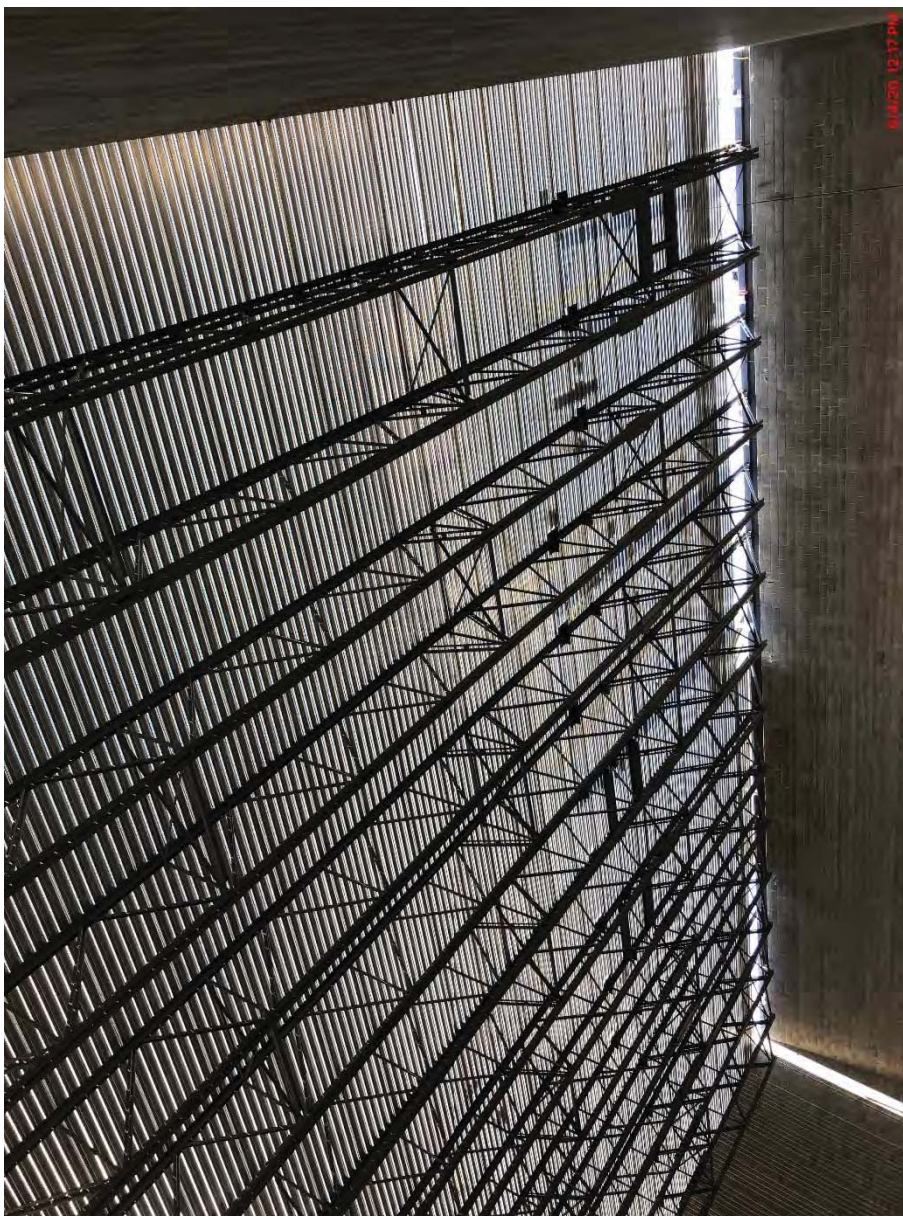


Photo 4: Steel Joists and decking have been placed on the auditorium.
