


REQUEST FOR PROPOSALS
For
Architectural Services for Four New (replacement) Schools

ATTACHMENT E

Project Schedule

POTENTIAL 2013 BOND SCHEDULE

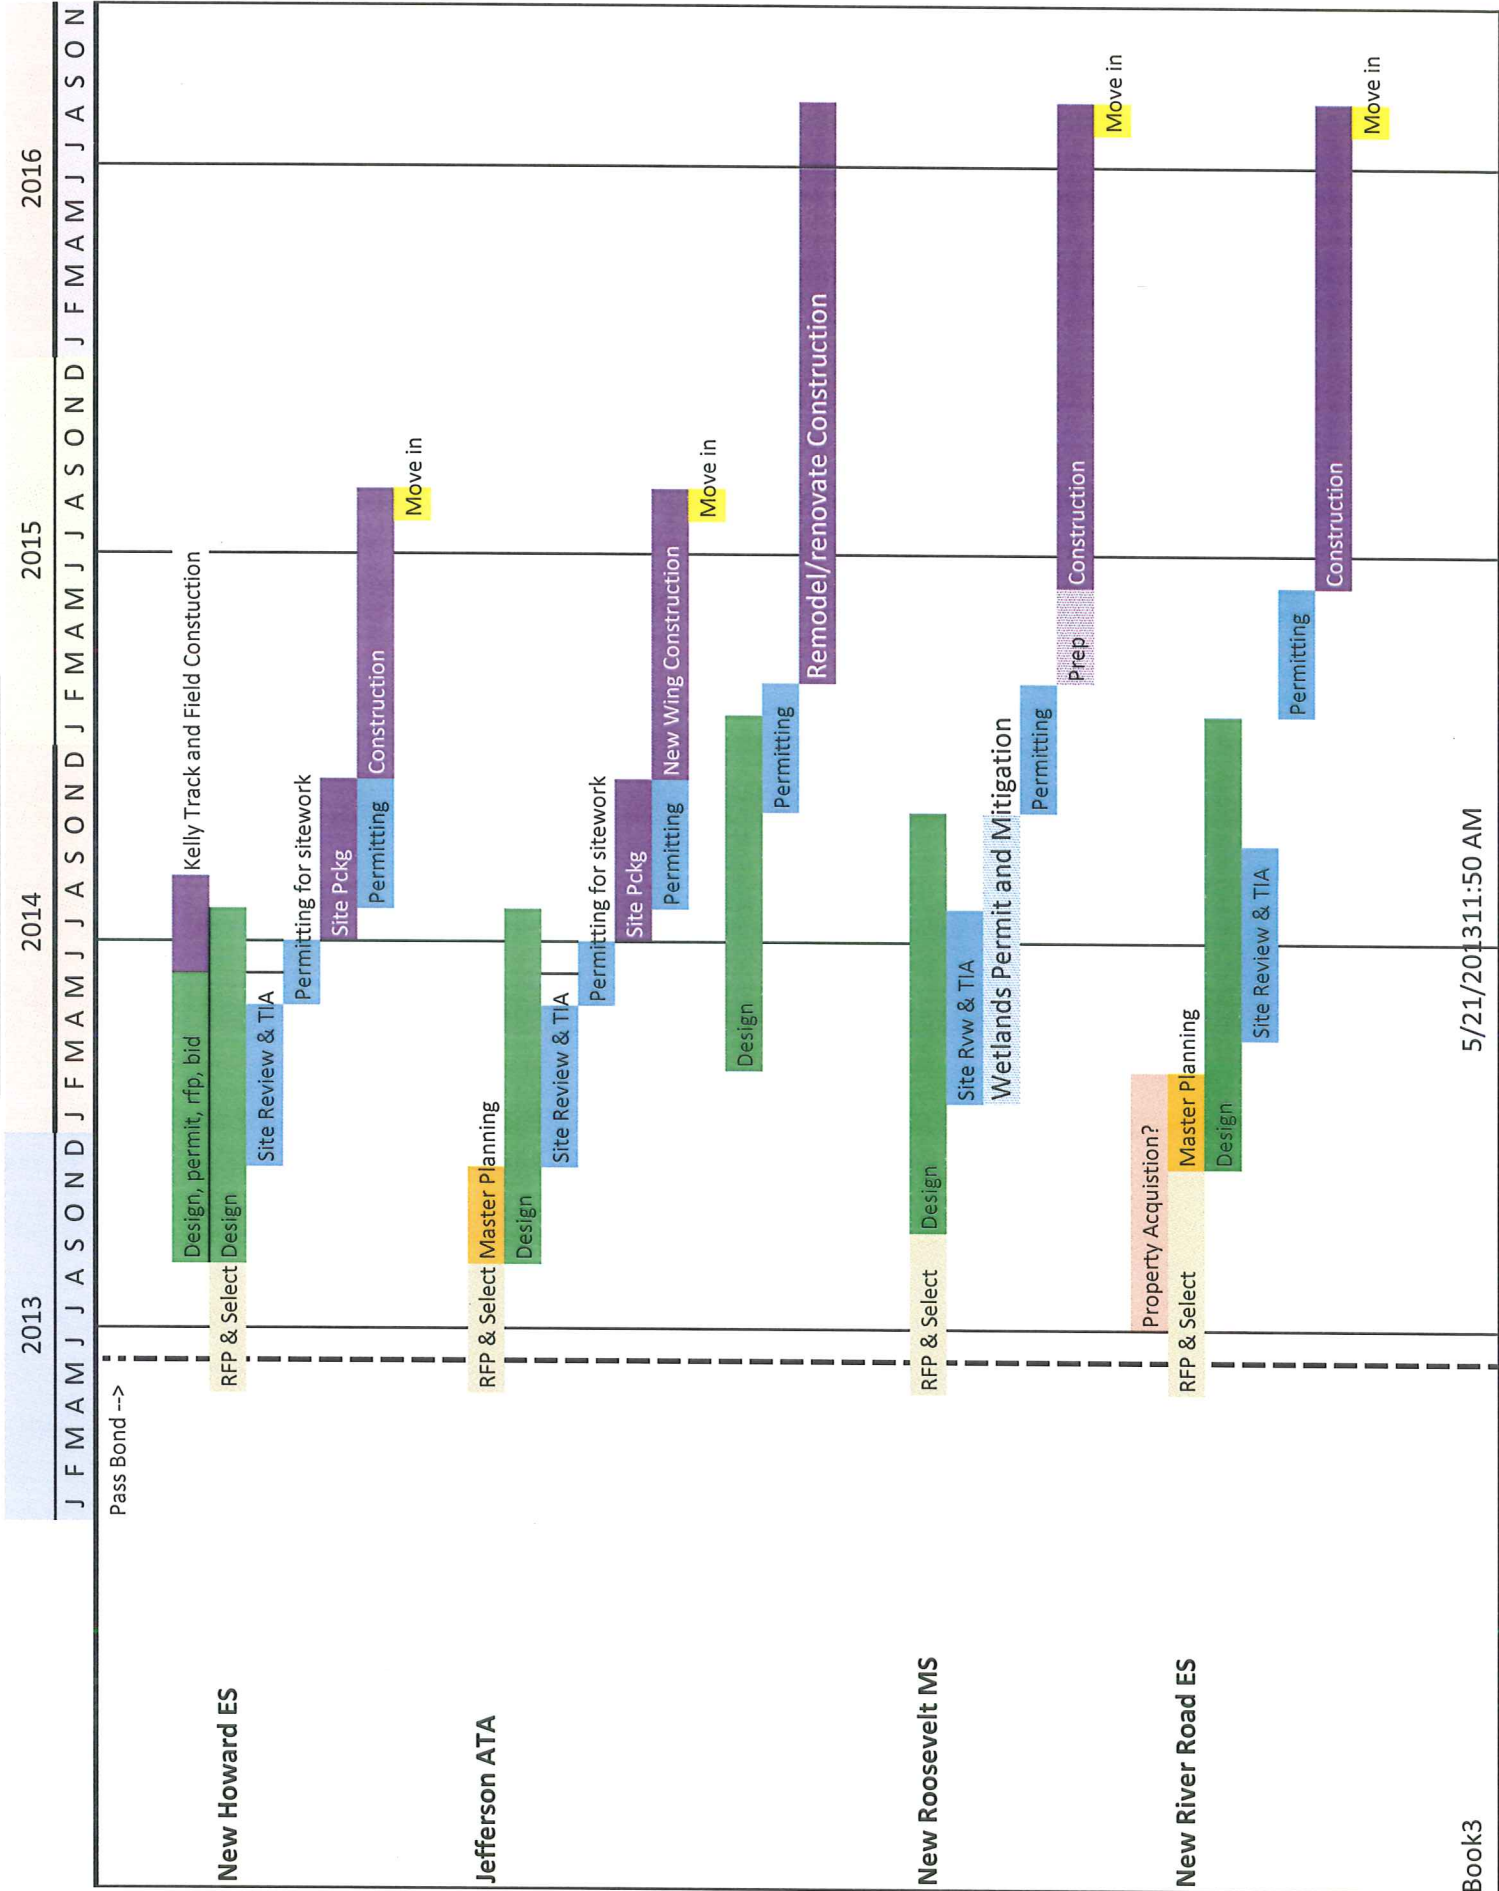

2013 BOND - MAJOR PROJECT SCHEDULE

| ACTIVITY | HOWARD ELEMENTARY SCHOOL | JEFFERSON MIDDLE SCHOOL NEW WING | JEFFERSON MIDDLE SCHOOL RENOVATION/REMODEL | ROOSEVELT MIDDLE SCHOOL | RIVER ROAD ELEM SCHOOL |
|--|--------------------------|-------------------------------------|---|-------------------------|------------------------|
| Begin Programming and Schematic Design | 08/20/13 | 08/20/13 | 08/20/13 | 10/01/13 | 12/02/13 |
| Submit Site Review Package to City of Eugene | 11/26/13 | 11/26/13 | 11/26/13 | 02/03/14 | 04/01/14 |
| Design Development Complete | 01/31/14 | 01/31/14 | 05/30/15 | | |
| Submit Wetlands Permit and Mitigation Plan | | | | 02/03/14 | |
| Sitework Documents Complete - Plan Check | 04/14/14 | 04/14/14 | | | |
| Submit for Sitework Permit | 04/28/14 | 04/28/14 | | | |
| Advertise for Bids - Sitework | 06/01/14 | 06/01/14 | | | |
| Bid - Sitework | 06/17/14 | 06/17/14 | | | |
| Notice to Proceed - Sitework | 06/30/14 | 06/30/14 | | | |
| Sitework Complete | 09/01/14 | 09/01/14 | | | |
| Construction Documents Complete - Plan Check | 07/01/14 | 07/01/14 | 11/28/15 | 10/01/14 | 01/05/15 |
| Submit for Building Permit | 08/04/14 | 08/04/14 | 01/04/16 | 11/02/14 | 02/02/15 |
| Advertise for Bids | 10/19/14 | 10/19/14 | 03/20/16 | 01/24/15 | 03/22/15 |
| Bid | 11/10/14 | 11/11/14 | 04/12/16 | 02/16/15 | 04/14/15 |
| Notice to Proceed | 12/01/14 | 12/01/14 | 05/03/16 | 03/01/15 | 05/01/15 |
| Substantial Completion - Building | 07/29/15 | 07/29/15 | 07/25/16 | 07/01/16 | 07/01/16 |
| Substantial Completion of Majority of Site | 08/11/15 | | 08/08/16 | 08/01/16 | 08/01/16 |
