



# Huntington Beach City School District



Board Meeting Presentation – Sowers Middle School

February 07, 2023

# Agenda



## A. Sowers MS Update

### 1. Construction Phase Progress




# Status of Sowers Middle School Project



## 1. Construction Phase Progress


- AMS Buildings Progress – Modular buildings 500 and 700 are complete; building 600 nearly complete; building 800 is partially complete and building 400 is in the early stages of completion
- Underground utility and infrastructure installation is in progress
- Furniture has been ordered except for the food commons and administration building
- Pile Progress - See next slide

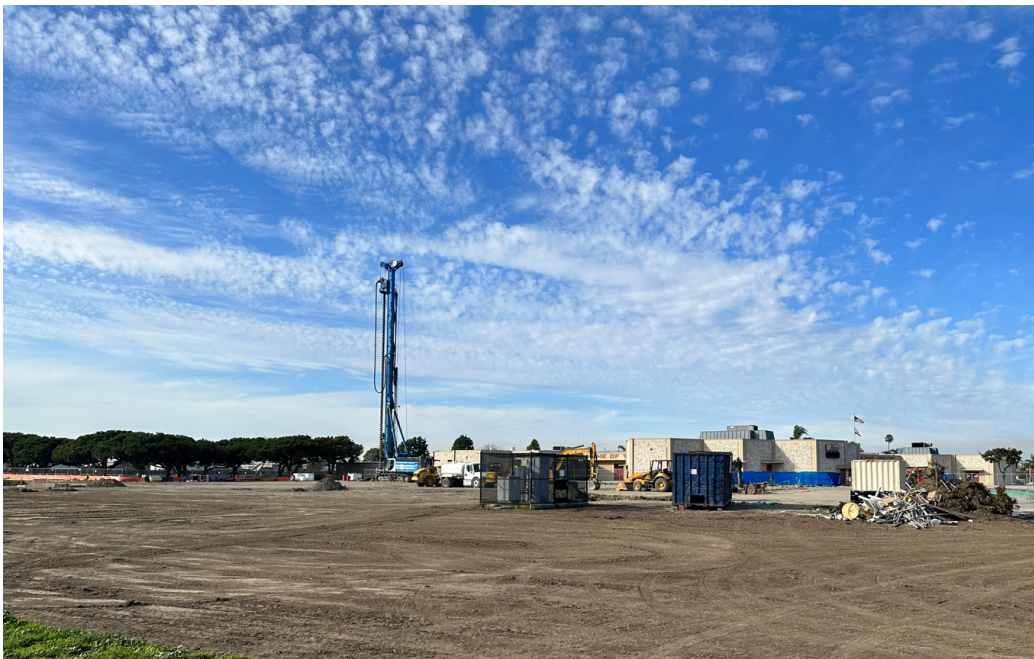

# Status of Sowers Middle School Project



## 1. Construction Phase Progress - Piles

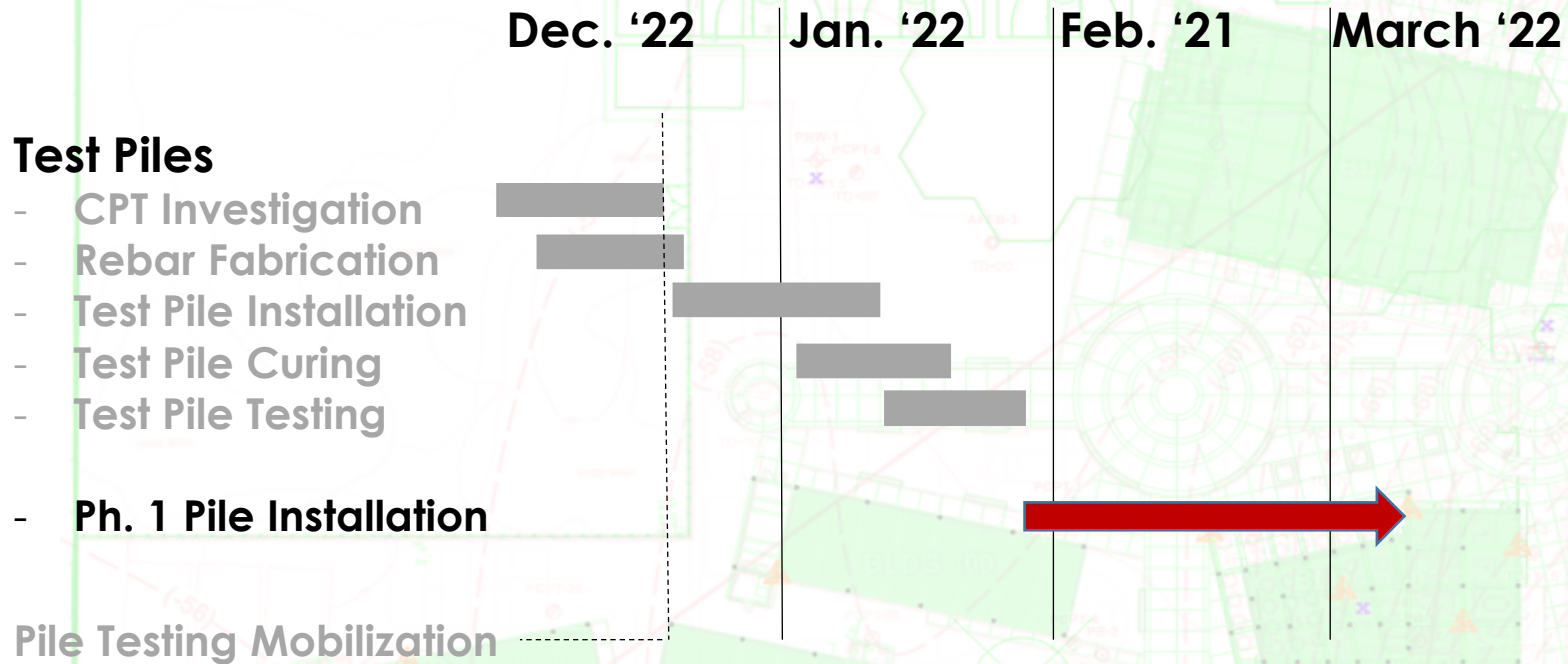

# Q & A



**Brian Whitmore, AIA, LEED** [brianw@studio-architects.com](mailto:brianw@studio-architects.com) 916-626-1303  
President/ CEO – Studio W Architects

**Michael Henning, AIA, LEED** [michaelh@studiow-architects.com](mailto:michaelh@studiow-architects.com) 949-293-2524  
Associate Principal – Studio W Architects

**Tony Pacheco Taylor, AIA, LEED** [tonyp@studiow-architects.com](mailto:tonyp@studiow-architects.com) 949-880-7230  
Client Leader, Associate – Studio W Architects
