

1789750 - Baldwinsville 2016 Capital Improvements Project



Multiple Building Sites Baldwinsville, NY 13027



Date Wed 08/01/2018

Job # 1789750

Prepared By Matthew Herbert

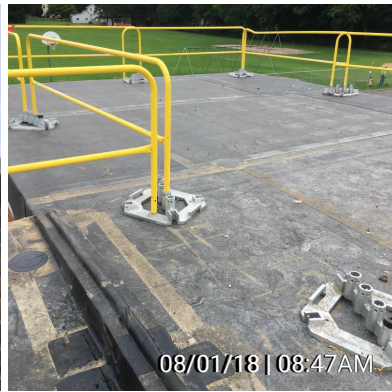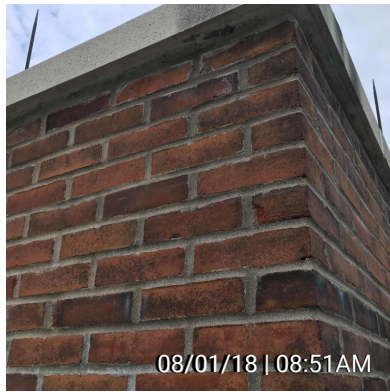

Weather

7:00 AM

73°

Partly Cloudy

Wind: 7 MPH | Precipitation: .0" | Humidity: 82%

12:00 PM

79°

Mostly Cloudy

Wind: 11 MPH | Precipitation: .0" | Humidity: 74%

3:00 PM

80°

Mostly Cloudy

Wind: 5 MPH | Precipitation: .01" | Humidity: 77%

Work Logs

Name	Description	Quantity	Hours	Hours To Date
AppelOsborne		0	0	29
CME Associates (Concrete)		0	0	8
CME Associates (Geotechnical)		0	0	186
Total		0	0	691

Notes, Issues, Concerns

1. VBE Roof:

Details work at chimneys and cafeteria wall. Expansion joints. Interior cleaning. General sight cleaning and preparation for demobilization. Reconnect rooftop condensers at north wing.

Bob Marketta | 08/01/18 | 08:56AM

2. Transportation Center:

Lan-Co. - continued storm piping installation near fuel island. Seeded aquatic bench area with specialized seeding.

Matthew Herbert | 08/01/18 | 03:02PM

3. Durgee:

Lan-Co. - final grading and seeding of running path.

Matthew Herbert | 08/01/18 | 03:02PM

Quality Control Observations

1. Noted on site that the underdrain for the gutter will have to be attached to the storm manholes using an internal coupling connection rather than running he pipe directly into he manhole. The manholes were cast with exactly a 4" opening meant for that pipe, which means the pipe does not fit.



Matthew Herbert | 08/02/18 | 08:00AM

Survey

Questions	N/A	No	Yes	Description
1. Any Time and Material work completed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2. Any Change Order work Completed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3. Any accidents on site today?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4. Any schedule delays occur?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5. Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6. Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7. Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
8. Any equipment on site?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Excavator - 3 Bulldozer - 4 Roller - 1 Field Dump Truck - 1 Front Loader - 1

Matthew Herbert | 08/02/18 | 07:56AM

Attachments

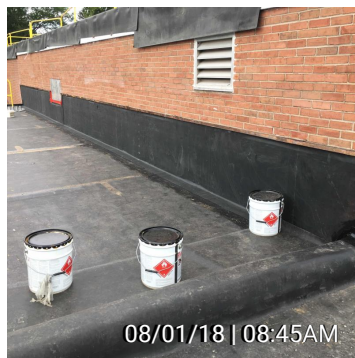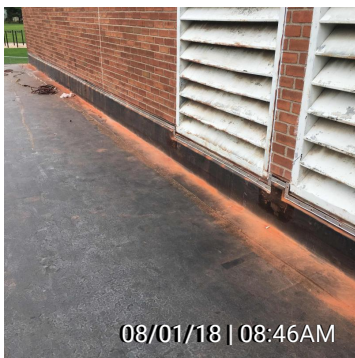



A handwritten signature in black ink, appearing to read 'M. Herbert', positioned above a horizontal line.

I, Matthew Herbert, have reviewed and completed this report.

Matthew Herbert | 08/02/18 | 08:01AM

SUBCONTRACTOR REPORTS



Wed 08/01/2018

1789750 - Baldwinsville 2016 Capital Improvements Project: Multiple Building Sites Baldwinsville, NY 13027

Name	Description	Quantity	Hours	Hours To Date
1. Lan-Co Companies	Continued installing storm sewer	5	40.0	4348.75
2. Myriad Electric	Inactive	0	0.0	58.00
3. J&B Installations, Inc.		12	96.0	4137.00
Subtotal		17	136	8543.75
Grand Total (Includes Work Log Total)		17	136	9234.75
