

Week Summary

12/01/19 - 12/07/19

[1789750 - Baldwinsville 2016
Capital Improvements Project -
Baker High School Kitchen
Renovation](#)

Job #: 1789750

120
Man Days

960
Hours

0
Materials

[1789750 - Baldwinsville 2016
Capital Improvements Project -
New Transportation Center](#)

Job #: 1789750

105
Man Days

836
Hours

0
Materials

Baker High School Kitchen Renovation



[View All Photos](#)

Detailed Stats December Week 1 Stats (12/01/19 - 12/07/19)

120
Man Days

960
Hours


All Time Stats

1396
Man Days


11165
Hours

Manpower ● LeChase Construction Services ● All Collaborators

[Full Manpower Report](#)

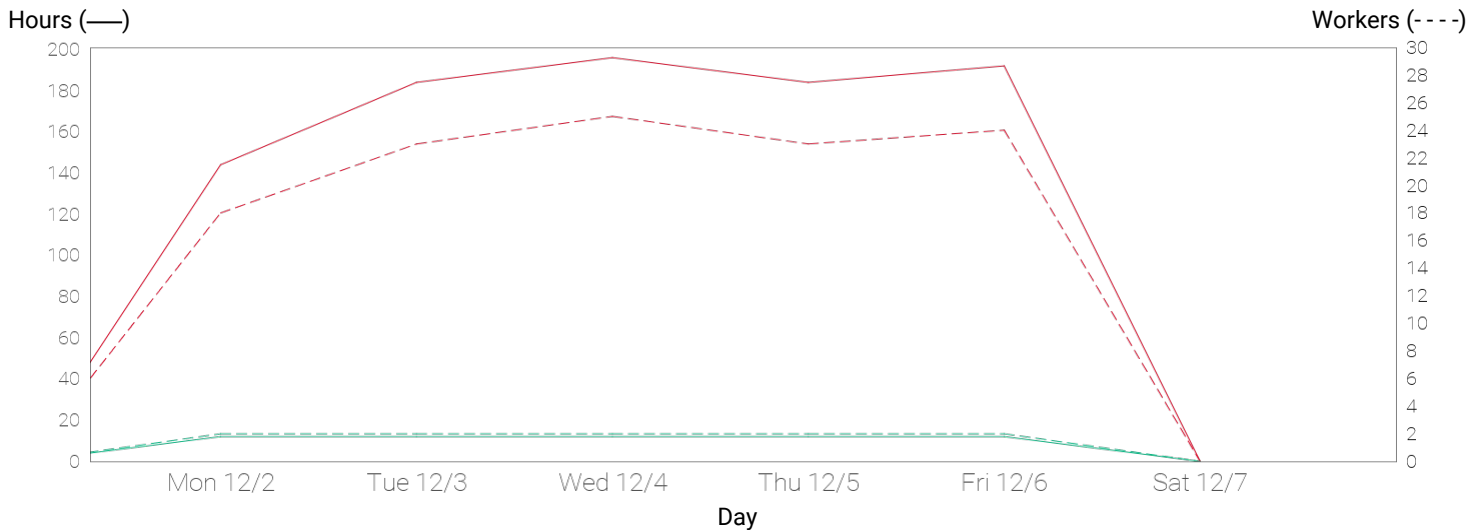

Monday 12/02/19

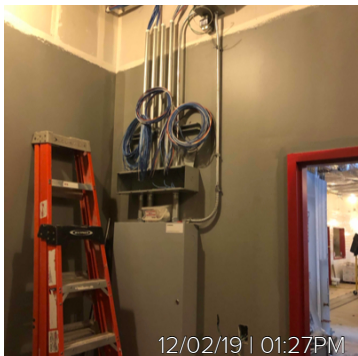




Tuesday 12/03/19



Wednesday 12/04/19



Thursday 12/05/19

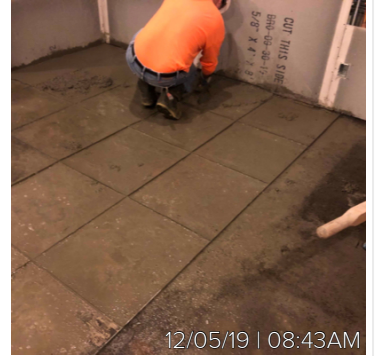

Friday 12/06/19



Detailed Stats


Company	Man Days	Manpower hours
LeChase Construction Services	8	60
Erie Mechanical Contractors, Inc.	35	280
Patricia Electric	17	136
S J Thomas Co Inc	61	484
Week Total	120	960
All Time Total	1396	11165

Full Manpower Report (Workers / Hrs)

Work Logs	Sun 12/01/19	Mon 12/02/19	Tue 12/03/19	Wed 12/04/19	Thu 12/05/19	Fri 12/06/19	Sat 12/07/19	Week Total

LeChase Construction Services	0 / 0	2 / 12	2 / 12	2 / 12	2 / 12	2 / 12	0 / 0	10 / 60
Bob Marketta	0 / 0	1 / 4	1 / 4	1 / 4	1 / 4	1 / 4	0 / 0	5 / 20
Donald Banks	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	5 / 40
Erie Mechanical Contractors, Inc.	0 / 0	7 / 56	7 / 56	7 / 56	7 / 56	7 / 56	0 / 0	35 / 280
Bill Ratnour	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	5 / 40
Chris herbert	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	5 / 40
Dave Root	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	5 / 40
Jason Ratnour	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	5 / 40
Jay Johnson	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	5 / 40
Jeremy Nicholas	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	5 / 40
Scott macmaster	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	5 / 40
Patricia Electric	0 / 0	4 / 32	3 / 24	3 / 24	3 / 24	4 / 32	0 / 0	17 / 136
Fire alarm/lighting	0 / 0	4 / 32	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	4 / 32
Install conduit/lighting	0 / 0	0 / 0	3 / 24	3 / 24	0 / 0	0 / 0	0 / 0	6 / 48
Install conduit/lighting/branch circuits	0 / 0	0 / 0	0 / 0	0 / 0	3 / 24	4 / 32	0 / 0	7 / 56
S J Thomas Co Inc	0 / 0	7 / 56	13 / 104	15 / 116	13 / 104	13 / 104	0 / 0	61 / 484
Dick Tile	0 / 0	4 / 32	11 / 88	11 / 88	11 / 88	11 / 88	0 / 0	48 / 384
Sherman Construction	0 / 0	3 / 24	2 / 16	2 / 16	2 / 16	2 / 16	0 / 0	11 / 88
View-Tech	0 / 0	0 / 0	0 / 0	2 / 12	0 / 0	0 / 0	0 / 0	2 / 12
Day Total	0 / 0	20 / 156	25 / 196	27 / 208	25 / 196	26 / 204	0 / 0	123 / 960

Transportation Center



[View All Photos](#)

[Detailed Stats](#) **December Week 1 Stats (12/01/19 - 12/07/19)**

105
Man Days


836
Hours

All Time Stats

6662
Man Days

53292
Hours

[Full Manpower Report](#) **Manpower** ● LeChase Construction Services ● All Collaborators




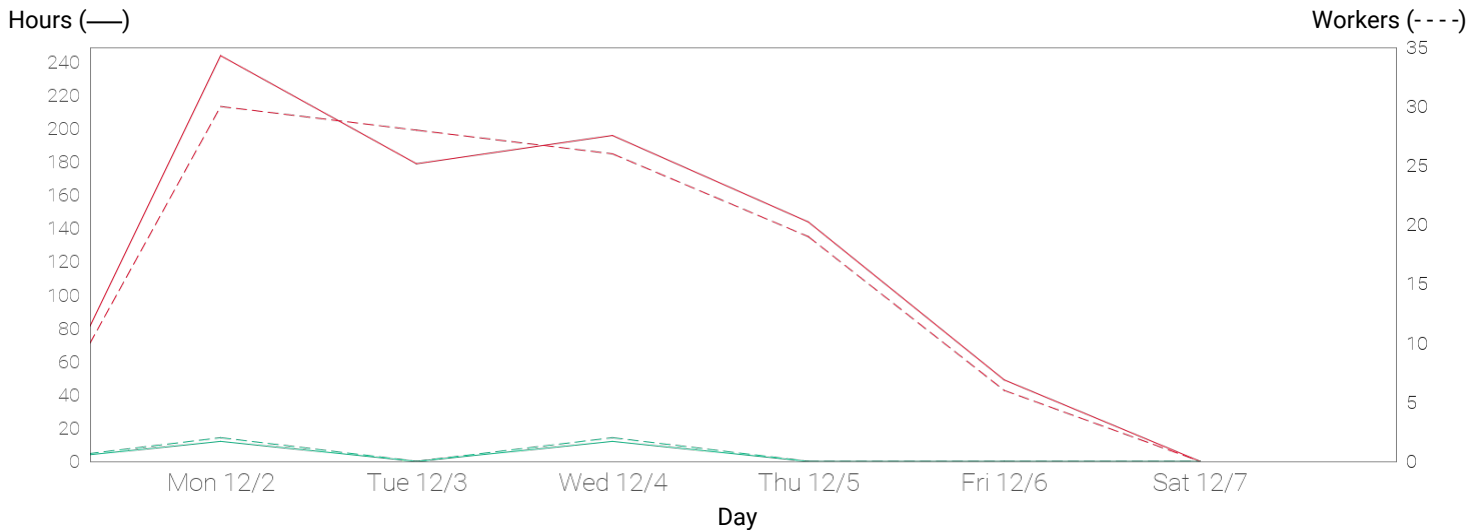


Monday 12/02/19





Tuesday 12/03/19

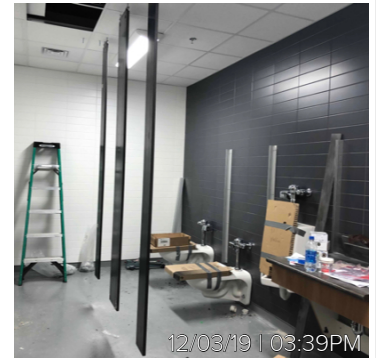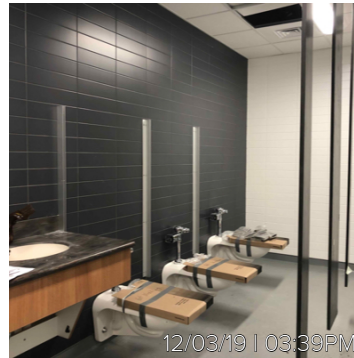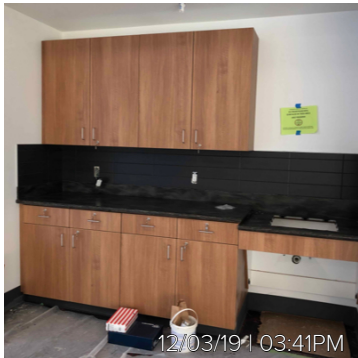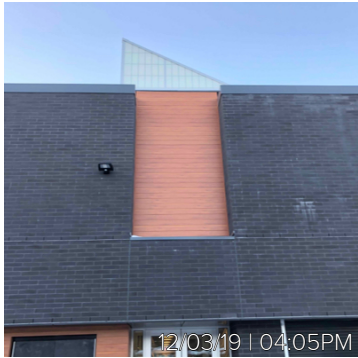

Detailed Stats

Company	Man Days	Manpower hours
LeChase Construction Services	3	24
Erie Mechanical Contractors, Inc.	14	113
Knapp Electric	8	64
Lawman Heating & Cooling	28	224
MCK Building Associates Inc	51	411
Week Total	105	836
All Time Total	6662	53292

Full Manpower Report (Workers / Hrs)

Work Logs	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Week

	12/01/19	12/02/19	12/03/19	12/04/19	12/05/19	12/06/19	12/07/19	Total
LeChase Construction Services	0 / 0	2 / 12	0 / 0	2 / 12	0 / 0	0 / 0	0 / 0	4 / 24
Bob Marketta	0 / 0	1 / 4	0 / 0	1 / 4	0 / 0	0 / 0	0 / 0	2 / 8
Matthew Herbert	0 / 0	1 / 8	0 / 0	1 / 8	0 / 0	0 / 0	0 / 0	2 / 16
Erie Mechanical Contractors, Inc.	0 / 0	3 / 24	3 / 24	3 / 24	3 / 24	2 / 17	0 / 0	14 / 113
Erie Mechanical.	0 / 0	3 / 24	3 / 24	3 / 24	3 / 24	2 / 17	0 / 0	14 / 113
Knapp Electric	0 / 0	8 / 64	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	8 / 64
Knapp Electric Inc.	0 / 0	8 / 64	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	8 / 64
Lawman Heating & Cooling	0 / 0	6 / 48	6 / 48	6 / 48	6 / 48	4 / 32	0 / 0	28 / 224
Insulation	0 / 0	2 / 16	2 / 16	2 / 16	2 / 16	2 / 16	0 / 0	10 / 80
Lawman - Ductwork	0 / 0	2 / 16	2 / 16	2 / 16	2 / 16	0 / 0	0 / 0	8 / 64
Lawman - Piping	0 / 0	2 / 16	2 / 16	2 / 16	2 / 16	2 / 16	0 / 0	10 / 80
MCK Building Associates Inc	0 / 0	13 / 108	19 / 107	17 / 124	10 / 72	0 / 0	0 / 0	59 / 411
Al Mitchel	0 / 0	3 / 24	1 / 8	1 / 8	1 / 8	0 / 0	0 / 0	6 / 48
Arrow Contracting	0 / 0	0 / 0	1 / 1	0 / 0	0 / 0	0 / 0	0 / 0	1 / 1
B.R. Johnson	0 / 0	2 / 16	2 / 16	2 / 16	2 / 16	0 / 0	0 / 0	8 / 64
Commercial Painting	0 / 0	3 / 24	3 / 24	5 / 40	3 / 24	0 / 0	0 / 0	14 / 112
Edward Schalk & Son	0 / 0	1 / 8	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	1 / 8
Imperial Cleaning	0 / 0	0 / 0	0 / 0	2 / 12	0 / 0	0 / 0	0 / 0	2 / 12
Integrated Industrial Solutions	0 / 0	2 / 16	2 / 16	2 / 16	2 / 16	0 / 0	0 / 0	8 / 64
Kevin Bruno Inc.	0 / 0	0 / 0	5 / 10	0 / 0	0 / 0	0 / 0	0 / 0	5 / 10
Otis	0 / 0	2 / 20	2 / 20	2 / 20	2 / 8	0 / 0	0 / 0	8 / 68
Ward Steel	0 / 0	0 / 0	3 / 12	3 / 12	0 / 0	0 / 0	0 / 0	6 / 24
Day Total	0 / 0	32 / 256	28 / 179	28 / 208	19 / 144	6 / 49	0 / 0	113 / 836
