

# Week Summary

11/10/19 - 11/16/19

[1789750 - Baldwinsville 2016  
Capital Improvements Project -  
Baker High School Kitchen  
Renovation](#)

Job #: 1789750

**98**  
Workers

**750**  
Hours

**0**  
Materials

[1789750 - Baldwinsville 2016  
Capital Improvements Project -  
New Transportation Center](#)

Job #: 1789750

**111**  
Workers

**824**  
Hours

**0**  
Materials

Baker High School Kitchen Renovation



[View All Photos](#)

[Detailed Stats](#) November Week 3 Stats (11/10/19 - 11/16/19)

**98**  
Workers


**750**  
Hours

All Time Stats


**1206**  
Workers

**8742**  
Hours

[Full Manpower Report](#) Manpower ● LeChase Construction Services ● All Collaborators

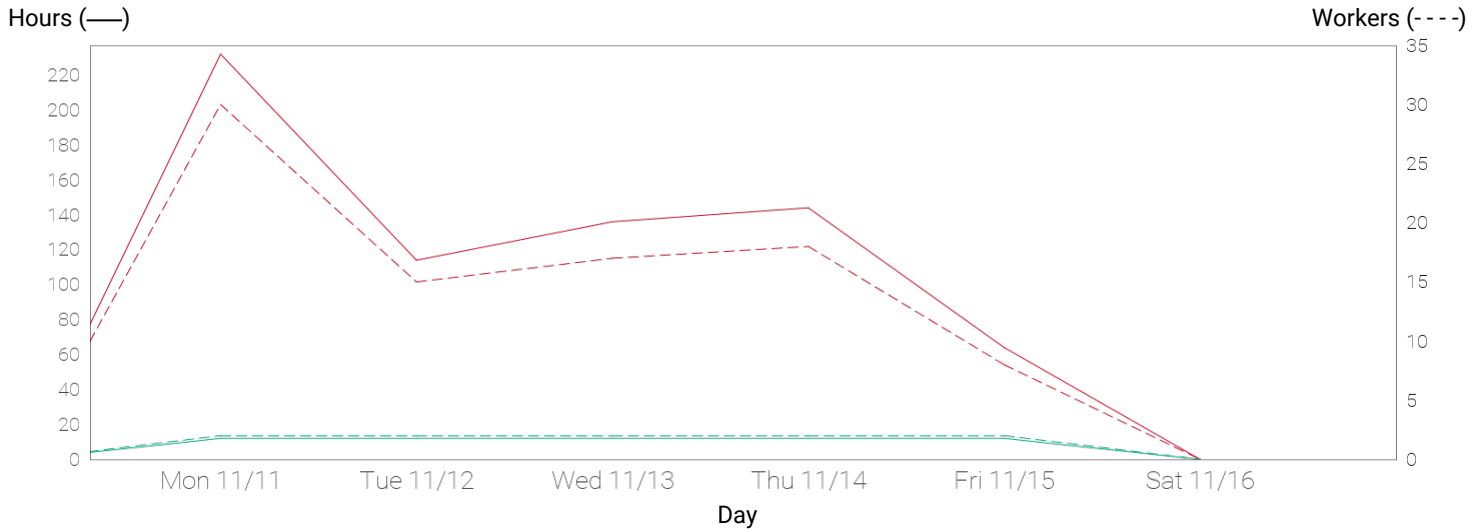

Monday 11/11/19

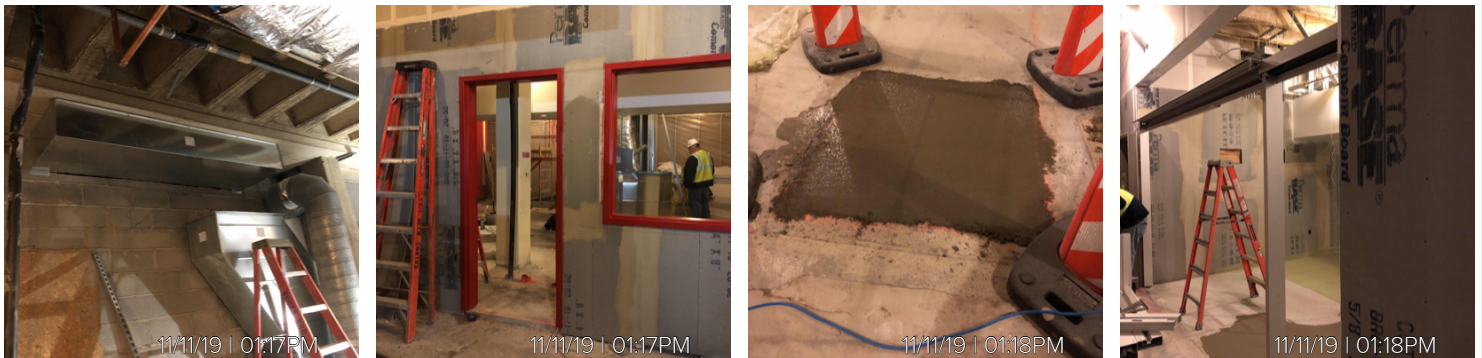





## Tuesday 11/12/19



## Wednesday 11/13/19



## Thursday 11/14/19





11/14/19 | 07:46AM



11/14/19 | 12:30PM



11/14/19 | 12:30PM



11/14/19 | 12:30PM



11/14/19 | 12:31PM



11/14/19 | 12:31PM



11/14/19 | 12:31PM




11/14/19 | 12:32PM


### Friday 11/15/19




11/15/19 | 03:09PM

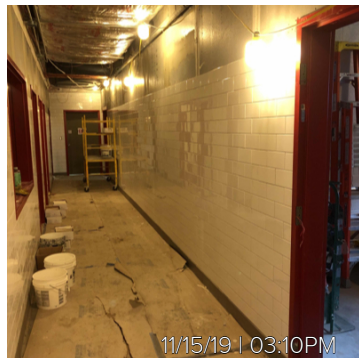


11/15/19 | 03:10PM

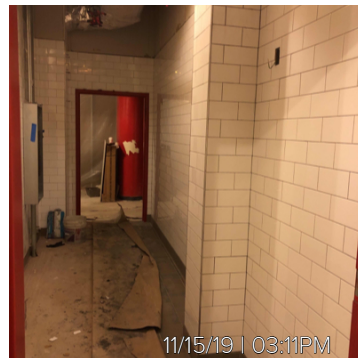

11/15/19 | 03:11PM

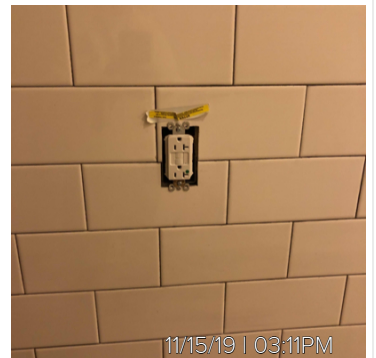

11/15/19 | 03:11PM

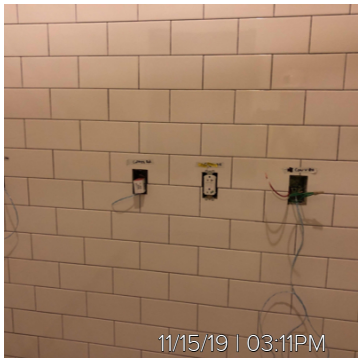

11/15/19 | 03:11PM



11/15/19 | 03:12PM



11/15/19 | 03:13PM



11/15/19 | 03:13PM

### Detailed Stats

Company	Workers	Manpower hours
LeChase Construction Services	10	60
Erie Mechanical Contractors, Inc.	19	152
Patricia Electric	20	160



S J Thomas Co Inc	49	378
Week Total	98	750
All Time Total	1206	8742

## Full Manpower Report (Workers / Hrs)

Work Logs	Sun 11/10/19	Mon 11/11/19	Tue 11/12/19	Wed 11/13/19	Thu 11/14/19	Fri 11/15/19	Sat 11/16/19	Week Total
<b>LeChase Construction Services</b>	0 / 0	2 / 12	2 / 12	2 / 12	2 / 12	2 / 12	0 / 0	10 / 60
Bob Marketta	0 / 0	1 / 4	1 / 4	1 / 4	1 / 4	1 / 4	0 / 0	5 / 20
Donald Banks	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	5 / 40
<b>Erie Mechanical Contractors, Inc.</b>	0 / 0	5 / 40	4 / 32	5 / 40	5 / 40	0 / 0	0 / 0	19 / 152
Bill Ratnour	0 / 0	1 / 8	0 / 0	1 / 8	1 / 8	0 / 0	0 / 0	3 / 24
Chris herbert	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	0 / 0	4 / 32
Dave Root	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	0 / 0	4 / 32
Jason Ratnour	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	0 / 0	4 / 32
Jay Johnson	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	0 / 0	4 / 32
<b>Patricia Electric</b>	0 / 0	5 / 40	3 / 24	6 / 48	6 / 48	0 / 0	0 / 0	20 / 160
Cafeteria/corridor receptacles and shutdown	0 / 0	5 / 40	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	5 / 40
Conduit install	0 / 0	0 / 0	0 / 0	6 / 48	0 / 0	0 / 0	0 / 0	6 / 48
Install conduit/pull wire	0 / 0	0 / 0	3 / 24	0 / 0	6 / 48	0 / 0	0 / 0	9 / 72
<b>S J Thomas Co Inc</b>	0 / 0	20 / 152	8 / 58	6 / 48	7 / 56	8 / 64	0 / 0	49 / 378
Aapex Contracting	0 / 0	4 / 48	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	4 / 48
Atlas Fence	0 / 0	2 / 6	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	2 / 6
Dick Tile	0 / 0	4 / 32	4 / 32	4 / 32	4 / 32	8 / 64	0 / 0	24 / 192
LA Painting	0 / 0	1 / 8	2 / 10	0 / 0	0 / 0	0 / 0	0 / 0	3 / 18
Sherman Construction	0 / 0	2 / 16	2 / 16	2 / 16	2 / 16	0 / 0	0 / 0	8 / 64
SJ Thomas Co	0 / 0	2 / 16	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	2 / 16
View-Tech/ASSA Abloy	0 / 0	3 / 24	0 / 0	0 / 0	1 / 8	0 / 0	0 / 0	4 / 32
Wayne Dalton	0 / 0	2 / 2	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	2 / 2
<b>Day Total</b>	0 / 0	32 / 244	17 / 126	19 / 148	20 / 156	10 / 76	0 / 0	98 / 750

Transportation Center



[View All Photos](#)

[Detailed Stats](#) November Week 3 Stats (11/10/19 - 11/16/19)

**111**  
Workers


**824**  
Hours

All Time Stats


**6586**  
Workers

**47508**  
Hours

[Full Manpower Report](#) Manpower ● LeChase Construction Services ● All Collaborators

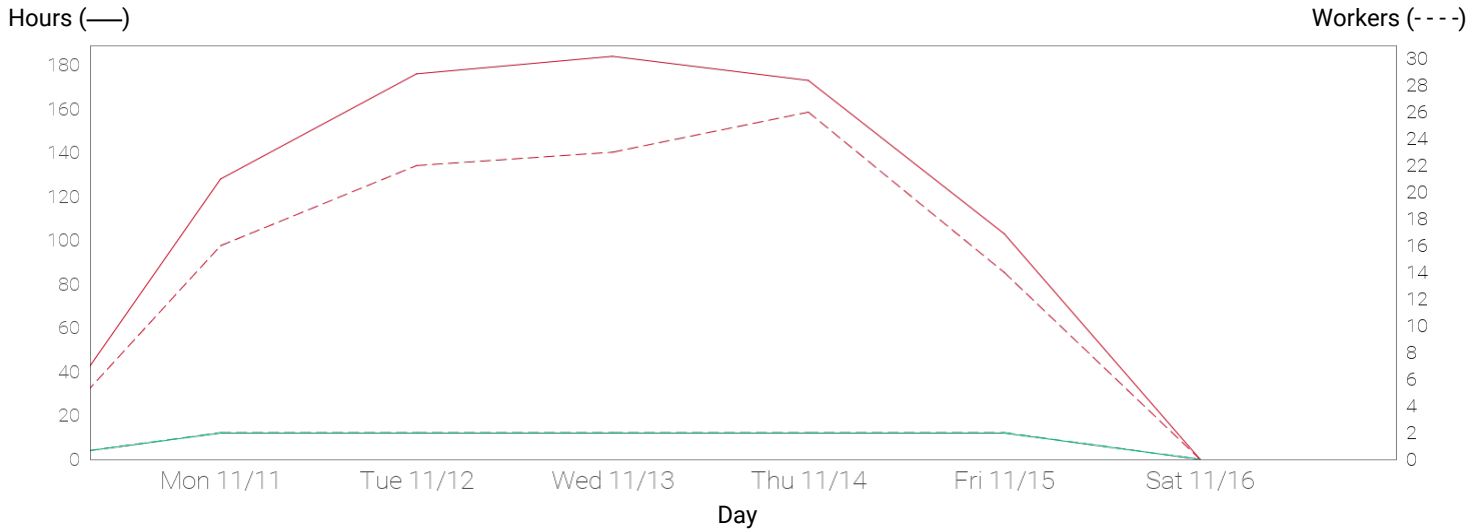

Monday 11/11/19

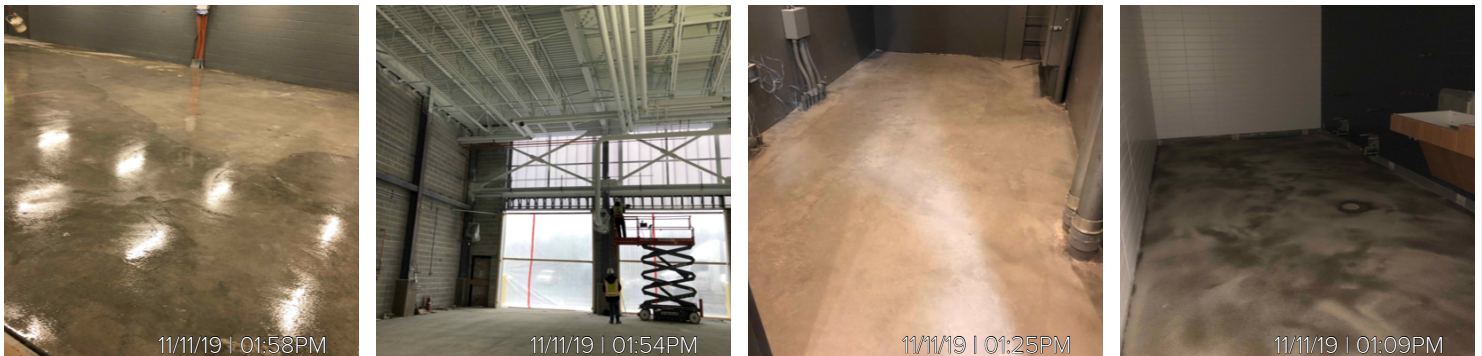







## Tuesday 11/12/19



## Wednesday 11/13/19

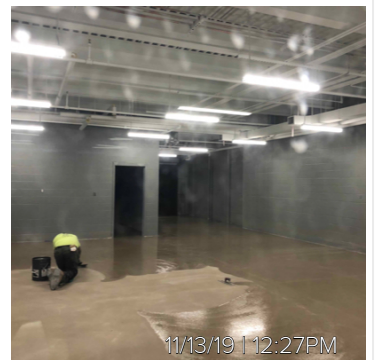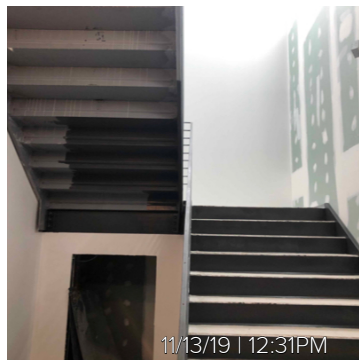









## Thursday 11/14/19



## Friday 11/15/19

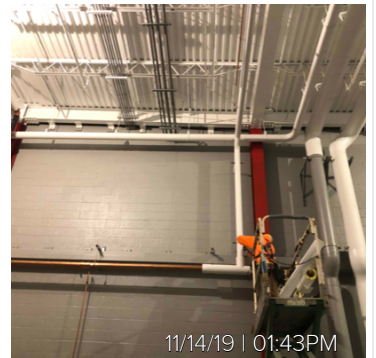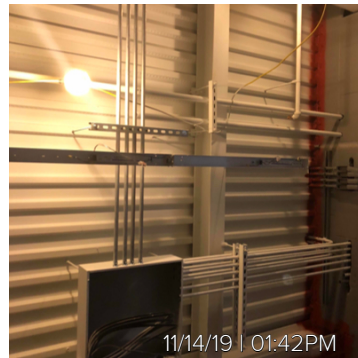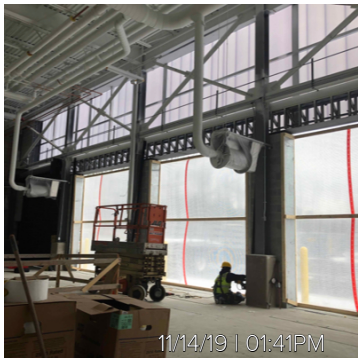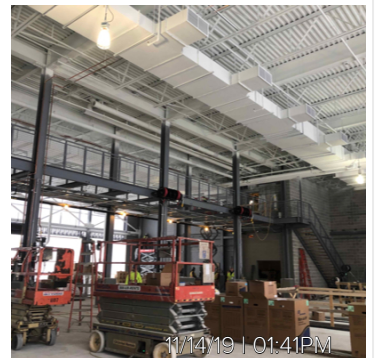

## Detailed Stats

Company

Workers

Manpower hours

LeChase Construction Services

10

60



Erie Mechanical Contractors, Inc.	15	120
Lawman Heating & Cooling	24	192
MCK Building Associates Inc	62	452
Titan Roofing	0	0
Week Total	111	824
<b>All Time Total</b>	<b>6586</b>	<b>47508</b>

## Full Manpower Report (Workers / Hrs)

Work Logs	Sun 11/10/19	Mon 11/11/19	Tue 11/12/19	Wed 11/13/19	Thu 11/14/19	Fri 11/15/19	Sat 11/16/19	Week Total
<b>LeChase Construction Services</b>	0 / 0	2 / 12	2 / 12	2 / 12	2 / 12	2 / 12	0 / 0	10 / 60
Bob Marketta	0 / 0	1 / 4	1 / 4	1 / 4	1 / 4	1 / 4	0 / 0	5 / 20
Matthew Herbert	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	5 / 40
<b>Erie Mechanical Contractors, Inc.</b>	0 / 0	0 / 0	2 / 16	4 / 32	6 / 48	3 / 24	0 / 0	15 / 120
Associated Fire Protection	0 / 0	0 / 0	0 / 0	1 / 8	0 / 0	0 / 0	0 / 0	1 / 8
Erie Mechanical.	0 / 0	0 / 0	2 / 16	3 / 24	3 / 24	3 / 24	0 / 0	11 / 88
Sabert insulation	0 / 0	0 / 0	0 / 0	0 / 0	3 / 24	0 / 0	0 / 0	3 / 24
<b>Lawman Heating &amp; Cooling</b>	0 / 0	6 / 48	7 / 56	8 / 64	3 / 24	0 / 0	0 / 0	24 / 192
Insulation	0 / 0	2 / 16	2 / 16	3 / 24	0 / 0	0 / 0	0 / 0	7 / 56
Lawman - Ductwork	0 / 0	2 / 16	2 / 16	2 / 16	1 / 8	0 / 0	0 / 0	7 / 56
Lawman - Piping	0 / 0	2 / 16	3 / 24	3 / 24	2 / 16	0 / 0	0 / 0	10 / 80
<b>MCK Building Associates Inc</b>	0 / 0	10 / 80	13 / 104	11 / 88	17 / 101	11 / 79	0 / 0	62 / 452
Commercial Painting	0 / 0	4 / 32	4 / 32	4 / 32	4 / 32	3 / 24	0 / 0	19 / 152
Edward Schalk & Son	0 / 0	1 / 8	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	1 / 8
Joe Baldwin Masonry	0 / 0	0 / 0	0 / 0	0 / 0	2 / 2	0 / 0	0 / 0	2 / 2
MCK Building Associates	0 / 0	0 / 0	2 / 16	2 / 16	2 / 16	2 / 16	0 / 0	8 / 64
Mullen Industrial	0 / 0	0 / 0	2 / 16	0 / 0	0 / 0	0 / 0	0 / 0	2 / 16
Oneida Flooring	0 / 0	0 / 0	0 / 0	0 / 0	1 / 1	0 / 0	0 / 0	1 / 1
Overhead Door	0 / 0	2 / 16	2 / 16	2 / 16	3 / 24	3 / 24	0 / 0	12 / 96
Palma Inc.	0 / 0	3 / 24	3 / 24	3 / 24	3 / 24	3 / 15	0 / 0	15 / 111
Ward Steel	0 / 0	0 / 0	0 / 0	0 / 0	2 / 2	0 / 0	0 / 0	2 / 2
Titan Roofing	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0
<b>Day Total</b>	0 / 0	18 / 140	24 / 188	25 / 196	28 / 185	16 / 115	0 / 0	111 / 824
