

Week Summary

11/17/19 - 11/23/19

[1789750 - Baldwinsville 2016
Capital Improvements Project -
Baker High School Kitchen
Renovation](#)

Job #: 1789750

105
Workers

794
Hours

0
Materials

[1789750 - Baldwinsville 2016
Capital Improvements Project -
New Transportation Center](#)

Job #: 1789750

98
Workers

751
Hours

0
Materials

Baker High School Kitchen Renovation



[View All Photos](#)

[Detailed Stats](#) November Week 4 Stats (11/17/19 - 11/23/19)

105
Workers


794
Hours

All Time Stats

1325
Workers

9648
Hours

[Full Manpower Report](#) Manpower ● LeChase Construction Services ● All Collaborators

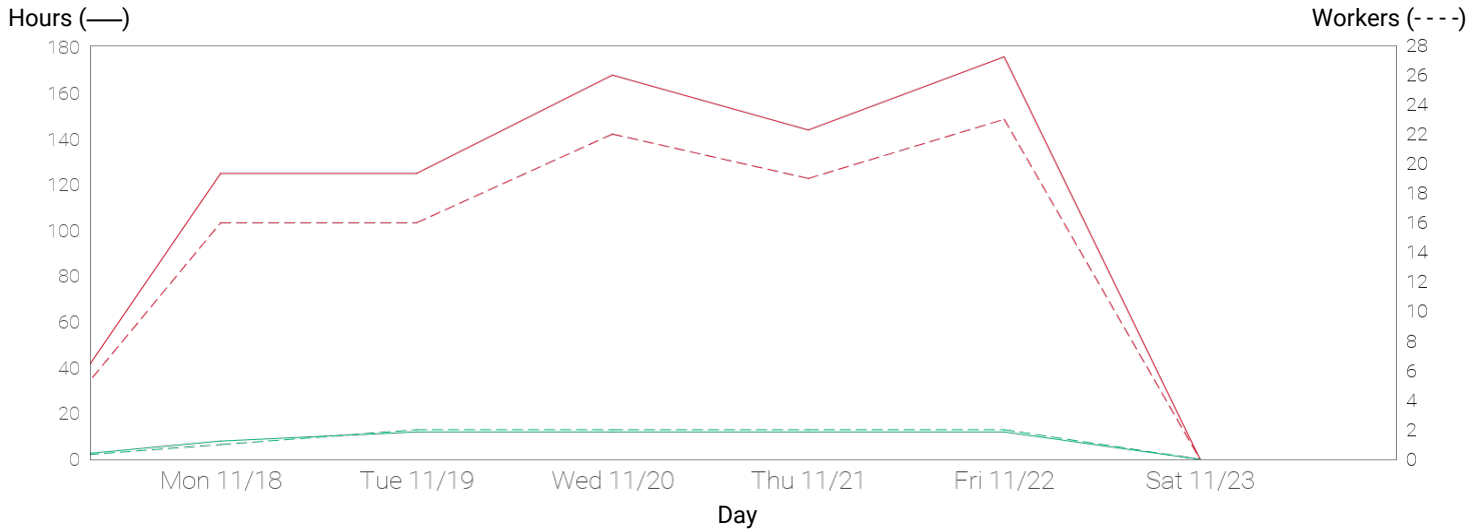


Tuesday 11/19/19





Wednesday 11/20/19

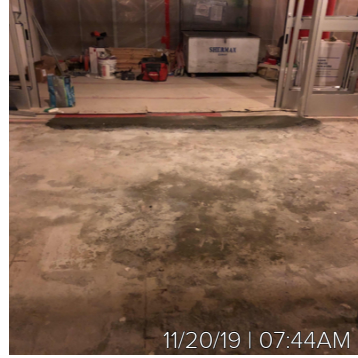

Thursday 11/21/19



Detailed Stats

Company

Workers

Manpower hours

LeChase Construction Services

9

56

Erie Mechanical Contractors, Inc.	32	256
Patricia Electric	25	191
S J Thomas Co Inc	39	291
Week Total	105	794
All Time Total	1325	9648

Full Manpower Report (Workers / Hrs)								
Work Logs	Sun 11/17/19	Mon 11/18/19	Tue 11/19/19	Wed 11/20/19	Thu 11/21/19	Fri 11/22/19	Sat 11/23/19	Week Total
LeChase Construction Services	0 / 0	1 / 8	2 / 12	2 / 12	2 / 12	2 / 12	0 / 0	9 / 56
Bob Marketta	0 / 0	1 / 8	1 / 4	1 / 4	1 / 4	1 / 4	0 / 0	5 / 24
Donald Banks	0 / 0	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	4 / 32
Erie Mechanical Contractors, Inc.	0 / 0	6 / 48	6 / 48	7 / 56	6 / 48	7 / 56	0 / 0	32 / 256
Bill Ratnour	0 / 0	0 / 0	0 / 0	1 / 8	1 / 8	1 / 8	0 / 0	3 / 24
Chris herbert	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	5 / 40
Cody ryan	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	5 / 40
Dave Root	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	5 / 40
Jason Ratnour	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	5 / 40
Jay Johnson	0 / 0	1 / 8	1 / 8	1 / 8	0 / 0	0 / 0	0 / 0	3 / 24
Jeremy Nicholas	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	1 / 8	0 / 0	1 / 8
Scott macmaster	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	5 / 40
Patricia Electric	0 / 0	4 / 32	4 / 29	6 / 42	5 / 40	6 / 48	0 / 0	25 / 191
Install conduit	0 / 0	4 / 32	4 / 29	0 / 0	0 / 0	0 / 0	0 / 0	8 / 61
Install conduit/pull wire	0 / 0	0 / 0	0 / 0	6 / 42	5 / 40	0 / 0	0 / 0	11 / 82
pull wire	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	6 / 48	0 / 0	6 / 48
S J Thomas Co Inc	0 / 0	6 / 45	6 / 48	9 / 70	8 / 56	10 / 72	0 / 0	39 / 291
Atlas Fence	0 / 0	0 / 0	0 / 0	1 / 2	0 / 0	0 / 0	0 / 0	1 / 2
Dick Tile	0 / 0	5 / 40	5 / 40	4 / 36	4 / 36	4 / 32	0 / 0	22 / 184
LaFace Construction - Masonry	0 / 0	0 / 0	0 / 0	2 / 16	0 / 0	0 / 0	0 / 0	2 / 16
Sherman	0 / 0	0 / 0	0 / 0	0 / 0	2 / 16	0 / 0	0 / 0	2 / 16
Sherman Construction	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	2 / 16	0 / 0	2 / 16
View-Tech	0 / 0	0 / 0	0 / 0	0 / 0	2 / 4	0 / 0	0 / 0	2 / 4
View-Tech/ASSA Abloy	0 / 0	1 / 5	1 / 8	2 / 16	0 / 0	4 / 24	0 / 0	8 / 53
Day Total	0 / 0	17 / 133	18 / 137	24 / 180	21 / 156	25 / 188	0 / 0	105 / 794

[Detailed Stats](#) **November Week 4 Stats (11/17/19 - 11/23/19)**

98
Workers


751
Hours

All Time Stats

7039
Workers

51181
Hours

[Full Manpower Report](#) **Manpower** ● LeChase Construction Services ● All Collaborators

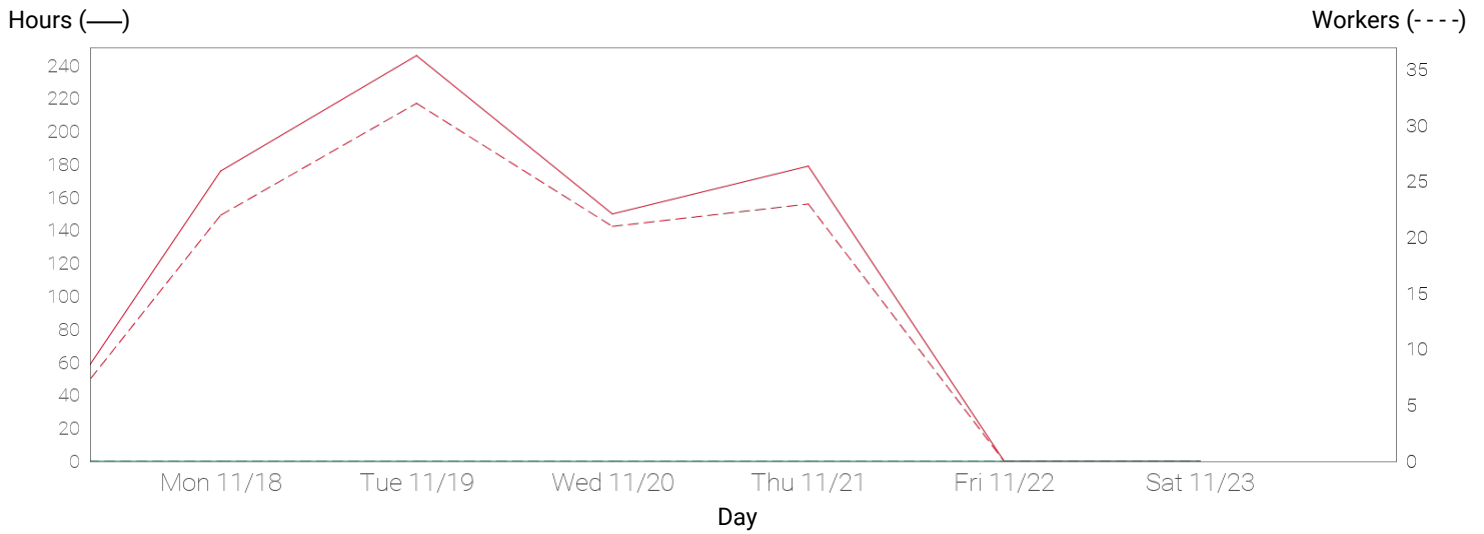

Detailed Stats

Company	Workers	Manpower hours
LeChase Construction Services	0	0
Erie Mechanical Contractors, Inc.	23	184
Knapp Electric	16	128
Lawman Heating & Cooling	14	112
MCK Building Associates Inc	45	327
Week Total	98	751
All Time Total	7039	51181

Full Manpower Report (Workers / Hrs)

Work Logs	Sun 11/17/19	Mon 11/18/19	Tue 11/19/19	Wed 11/20/19	Thu 11/21/19	Fri 11/22/19	Sat 11/23/19	Week Total
LeChase Construction	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0

Services								
Erie Mechanical Contractors, Inc.	0 / 0	3 / 24	7 / 56	5 / 40	8 / 64	0 / 0	0 / 0	23 / 184
Associated Fire Protection	0 / 0	0 / 0	2 / 16	0 / 0	2 / 16	0 / 0	0 / 0	4 / 32
Erie Mechanical.	0 / 0	3 / 24	3 / 24	2 / 16	3 / 24	0 / 0	0 / 0	11 / 88
Sabert insulation	0 / 0	0 / 0	2 / 16	3 / 24	3 / 24	0 / 0	0 / 0	8 / 64
Knapp Electric	0 / 0	7 / 56	9 / 72	0 / 0	0 / 0	0 / 0	0 / 0	16 / 128
Knapp Electric Inc.	0 / 0	7 / 56	9 / 72	0 / 0	0 / 0	0 / 0	0 / 0	16 / 128
Lawman Heating & Cooling	0 / 0	2 / 16	4 / 32	4 / 32	4 / 32	0 / 0	0 / 0	14 / 112
Insulation	0 / 0	0 / 0	2 / 16	2 / 16	2 / 16	0 / 0	0 / 0	6 / 48
Lawman - Piping	0 / 0	2 / 16	2 / 16	2 / 16	2 / 16	0 / 0	0 / 0	8 / 64
MCK Building Associates Inc	0 / 0	10 / 80	12 / 86	12 / 78	11 / 83	0 / 0	0 / 0	45 / 327
Arrow Contracting	0 / 0	1 / 8	1 / 8	1 / 8	1 / 8	0 / 0	0 / 0	4 / 32
B.R. Johnson	0 / 0	0 / 0	0 / 0	2 / 6	0 / 0	0 / 0	0 / 0	2 / 6
Commercial Painting	0 / 0	2 / 16	4 / 32	2 / 16	2 / 16	0 / 0	0 / 0	10 / 80
Gitzen	0 / 0	2 / 16	2 / 16	2 / 16	2 / 16	0 / 0	0 / 0	8 / 64
MCK Building Associates	0 / 0	2 / 16	0 / 0	0 / 0	1 / 8	0 / 0	0 / 0	3 / 24
Oneida Flooring	0 / 0	0 / 0	0 / 0	2 / 8	1 / 8	0 / 0	0 / 0	3 / 16
Overhead Door	0 / 0	3 / 24	3 / 24	3 / 24	3 / 24	0 / 0	0 / 0	12 / 96
Rob Larobardier	0 / 0	0 / 0	0 / 0	0 / 0	1 / 3	0 / 0	0 / 0	1 / 3
Ward Steel	0 / 0	0 / 0	2 / 6	0 / 0	0 / 0	0 / 0	0 / 0	2 / 6
Day Total	0 / 0	22 / 176	32 / 246	21 / 150	23 / 179	0 / 0	0 / 0	98 / 751
