



[View All Photos](#)

[Detailed Stats](#) **May Week 4 Stats (05/19/19 - 05/25/19)**

144
Workers


1109
Hours

All Time Stats

3597
Workers

26154
Hours

[Full Manpower Report](#) **Manpower** ● LeChase Construction Services ■ All Collaborators

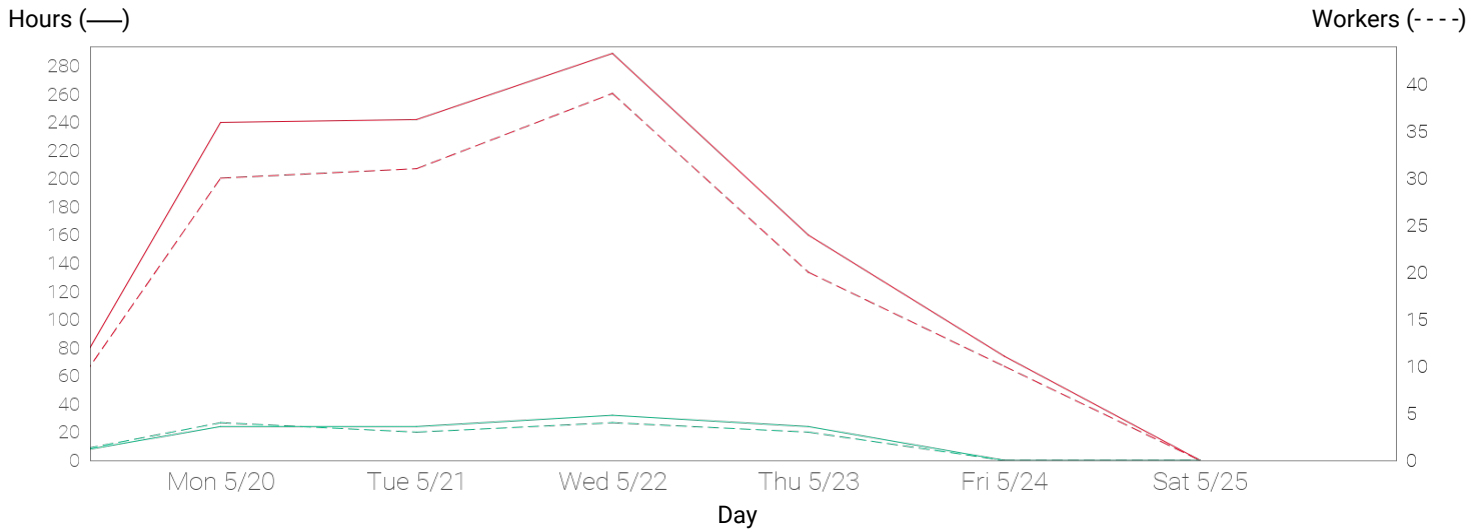


Monday 05/20/19









Tuesday 05/21/19

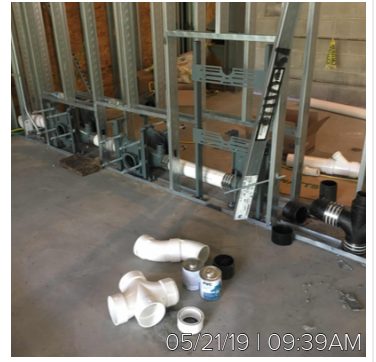

Wednesday 05/22/19

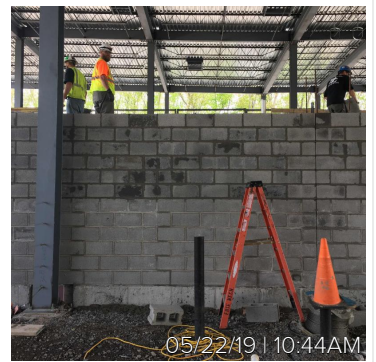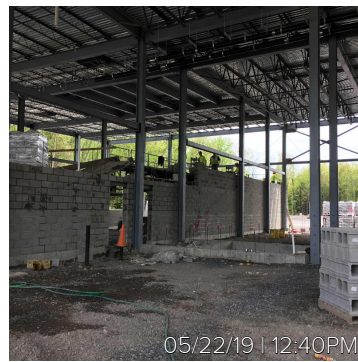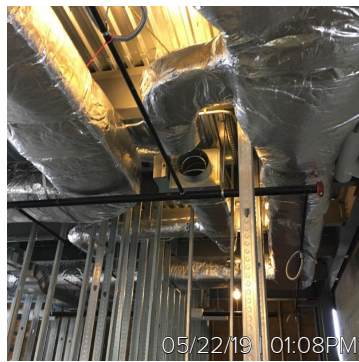

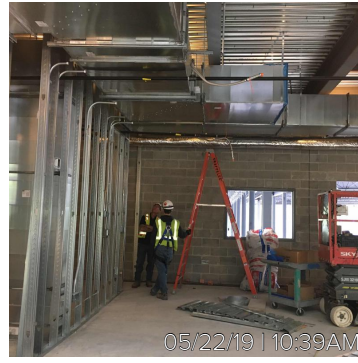

Thursday 05/23/19



Friday 05/24/19





Detailed Stats

Company	Workers	Manpower hours
LeChase Construction Services	14	104
Erie Mechanical Contractors, Inc.	18	140
Knapp Electric	12	96
Lan-Co Companies	0	0
Lawman Heating & Cooling	31	230
MCK Building Associates Inc	48	371
Myriad Electric	0	0
Titan Roofing	21	168
Week Total	144	1109
All Time Total	3597	26154

Full Manpower Report (Workers / Hrs)

Work Logs	Sun 05/19/19	Mon 05/20/19	Tue 05/21/19	Wed 05/22/19	Thu 05/23/19	Fri 05/24/19	Sat 05/25/19	Week Total
LeChase Construction Services	0 / 0	4 / 24	3 / 24	4 / 32	3 / 24	0 / 0	0 / 0	14 / 104
CME Associates (Concrete)	0 / 0	1 / 4	1 / 8	2 / 16	1 / 8	0 / 0	0 / 0	5 / 36
CME Associates (Steel)	0 / 0	1 / 4	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	1 / 4
LeChase Construction	0 / 0	2 / 16	2 / 16	2 / 16	2 / 16	0 / 0	0 / 0	8 / 64
Erie Mechanical Contractors, Inc.	0 / 0	2 / 16	2 / 16	6 / 48	6 / 48	2 / 12	0 / 0	18 / 140
Erie Mechanical.	0 / 0	2 / 16	2 / 16	2 / 16	2 / 16	2 / 12	0 / 0	10 / 76
Sabert insulation	0 / 0	0 / 0	0 / 0	4 / 32	4 / 32	0 / 0	0 / 0	8 / 64
Knapp Electric	0 / 0	4 / 32	4 / 32	4 / 32	0 / 0	0 / 0	0 / 0	12 / 96
Knapp Electric Inc.	0 / 0	4 / 32	4 / 32	4 / 32	0 / 0	0 / 0	0 / 0	12 / 96
Lan-Co Companies	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0
Lawman Heating & Cooling	0 / 0	6 / 48	5 / 40	7 / 40	7 / 56	6 / 46	0 / 0	31 / 230

Insulation	0 / 0	1 / 8	0 / 0	1 / 8	1 / 8	1 / 8	0 / 0	4 / 32
Lawman - Ductwork	0 / 0	2 / 16	2 / 16	2 / 0	2 / 16	2 / 14	0 / 0	10 / 62
Lawman - Piping	0 / 0	3 / 24	3 / 24	4 / 32	4 / 32	3 / 24	0 / 0	17 / 136
MCK Building Associates Inc	0 / 0	14 / 112	16 / 122	16 / 121	0 / 0	2 / 16	0 / 0	48 / 371
Edward Schalk & Son	0 / 0	2 / 16	2 / 16	2 / 16	0 / 0	2 / 16	0 / 0	8 / 64
Joe Baldwin Masonry	0 / 0	8 / 64	8 / 64	8 / 64	0 / 0	0 / 0	0 / 0	24 / 192
Paragon Masonry	0 / 0	0 / 0	2 / 10	1 / 1	0 / 0	0 / 0	0 / 0	3 / 11
Ward Steel	0 / 0	4 / 32	4 / 32	5 / 40	0 / 0	0 / 0	0 / 0	13 / 104
Myriad Electric	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0
Titan Roofing	0 / 0	4 / 32	4 / 32	6 / 48	7 / 56	0 / 0	0 / 0	21 / 168
Titan Roofing	0 / 0	4 / 32	4 / 32	6 / 48	7 / 56	0 / 0	0 / 0	21 / 168
Day Total	0 / 0	34 / 264	34 / 266	43 / 321	23 / 184	10 / 74	0 / 0	144 / 1109
