



[View All Photos](#)

[Detailed Stats](#) **May Week 5 Stats (05/26/19 - 06/01/19)**

176
Workers


1359
Hours

All Time Stats

3838
Workers

28013
Hours

[Full Manpower Report](#) **Manpower** ● LeChase Construction Services ■ All Collaborators

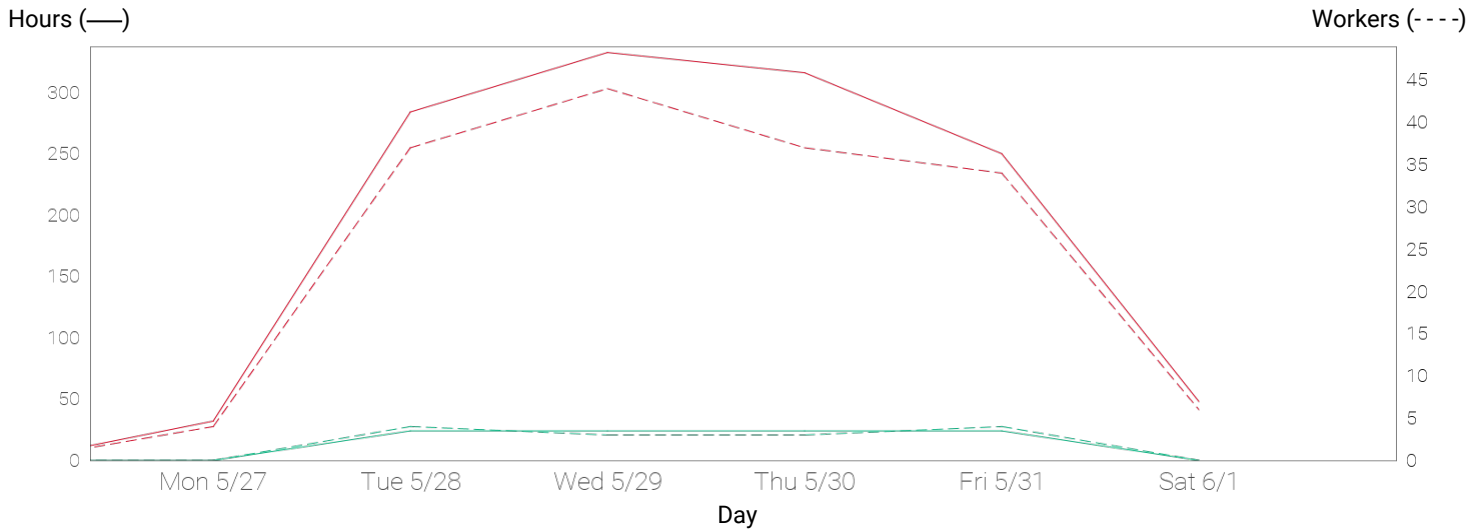


Tuesday 05/28/19







Wednesday 05/29/19

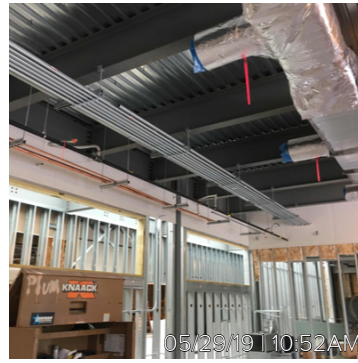

Thursday 05/30/19

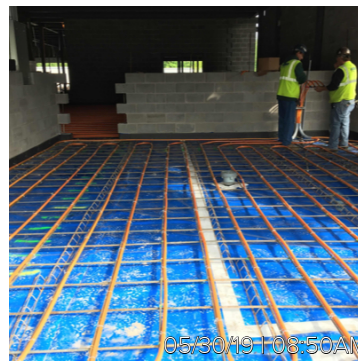

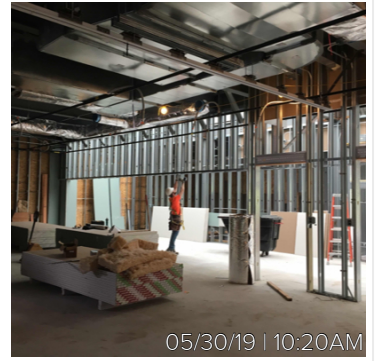

Friday 05/31/19



Detailed Stats

Company	Workers	Manpower hours
LeChase Construction Services	14	96
Erie Mechanical Contractors, Inc.	10	78
Knapp Electric	12	96
Lan-Co Companies	0	0
Lawman Heating & Cooling	33	232
MCK Building Associates Inc	73	553
Myriad Electric	0	0
Titan Roofing	34	304
Week Total	176	1359
All Time Total	3838	28013

Full Manpower Report (Workers / Hrs)

Work Logs	Sun 05/26/19	Mon 05/27/19	Tue 05/28/19	Wed 05/29/19	Thu 05/30/19	Fri 05/31/19	Sat 06/01/19	Week Total
LeChase Construction Services	0 / 0	0 / 0	4 / 24	3 / 24	3 / 24	4 / 24	0 / 0	14 / 96
CME Associates (Concrete)	0 / 0	0 / 0	1 / 4	1 / 8	1 / 8	1 / 4	0 / 0	4 / 24
CME Associates (Steel)	0 / 0	0 / 0	1 / 4	0 / 0	0 / 0	1 / 4	0 / 0	2 / 8
LeChase Construction	0 / 0	0 / 0	2 / 16	2 / 16	2 / 16	2 / 16	0 / 0	8 / 64
Erie Mechanical Contractors, Inc.	0 / 0	0 / 0	3 / 24	2 / 16	2 / 16	3 / 22	0 / 0	10 / 78
Associated Fire Protection	0 / 0	0 / 0	1 / 8	0 / 0	0 / 0	1 / 8	0 / 0	2 / 16
Erie Mechanical.	0 / 0	0 / 0	2 / 16	2 / 16	2 / 16	2 / 14	0 / 0	8 / 62
Knapp Electric	0 / 0	0 / 0	4 / 32	4 / 32	4 / 32	0 / 0	0 / 0	12 / 96
Knapp Electric Inc.	0 / 0	0 / 0	4 / 32	4 / 32	4 / 32	0 / 0	0 / 0	12 / 96
Lan-Co Companies	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0
Lawman Heating & Cooling	0 / 0	0 / 0	9 / 72	8 / 64	8 / 64	8 / 32	0 / 0	33 / 232
Insulation	0 / 0	0 / 0	1 / 8	0 / 0	0 / 0	0 / 0	0 / 0	1 / 8
Lawman - Ductwork	0 / 0	0 / 0	4 / 32	4 / 32	4 / 32	4 / 32	0 / 0	16 / 128
Lawman - Piping	0 / 0	0 / 0	4 / 32	4 / 32	4 / 32	4 / 0	0 / 0	16 / 96
MCK Building Associates Inc	0 / 0	0 / 0	21 / 156	22 / 157	15 / 120	15 / 120	0 / 0	73 / 553
B.R. Johnson	0 / 0	0 / 0	0 / 0	1 / 1	0 / 0	0 / 0	0 / 0	1 / 1
Edward Schalk & Son	0 / 0	0 / 0	2 / 16	3 / 24	1 / 8	1 / 8	0 / 0	7 / 56
Joe Baldwin Masonry	0 / 0	0 / 0	10 / 80	10 / 80	10 / 80	10 / 80	0 / 0	40 / 320
Paragon Masonry	0 / 0	0 / 0	4 / 20	3 / 12	0 / 0	0 / 0	0 / 0	7 / 32
Ward Steel	0 / 0	0 / 0	5 / 40	5 / 40	4 / 32	4 / 32	0 / 0	18 / 144
Myriad Electric	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0	0 / 0
Titan Roofing	0 / 0	4 / 32	0 / 0	8 / 64	8 / 84	8 / 76	6 / 48	34 / 304
Titan Roofing	0 / 0	4 / 32	0 / 0	8 / 64	8 / 84	8 / 76	6 / 48	34 / 304
Day Total	0 / 0	4 / 32	41 / 308	47 / 357	40 / 340	38 / 274	6 / 48	176 / 1359
