

Capital Projects Update

Report to the Board of Education

July 21, 2016

Hampton Street School

- Capital Reserve Project (November 2015)
 - Turf field
 - Turf track
 - Concession stand
 - Classroom additions/ stairway
 - Cafeteria/ kitchen/hallway/nurse's office
 - Bus lane
 - Playground modifications/ new surface
 - Storage facility (**Transfer to capital in 2016-17 budget)
- **Status-**
 - Architect is currently responding to initial SED review
 - Mechanical review is still 10 weeks away
- Revised Timeline
 - If SED approval by week of September 19, one month to bid hopeful for Board approval by October 20 meeting. If not November 10 meeting

Hampton Street continued

- SMART Bond monies
 - Old cafeteria pre-K classroom conversion
 - Separate permit number issued by SED
- Budget
 - A/C Music and Art rooms
- Completed Work
 - Capital Reserve project (November 2013)
 - Windows
 - Exterior doors
 - Masonry
 - HVAC
 - New unit ventilators and A/C in classrooms

Meadow Drive School


- 2016-2017 Budget- facility line
 - Playground Surface
 - Room 104 extension
 - Pre-K playground equipment and surface
- **Status-**
 - Plans complete, filing with SED
- Completed Work
 - Capital Reserve project (November 2013)
 - Windows
 - Exterior doors
 - Masonry
 - HVAC
 - New unit ventilators and A/C in classrooms

Jackson Avenue School

- Transfer to Capital 2015/2016
 - Windows
 - Exterior doors
 - **Status** Approved and waiting for Window manufacturer
 - Includes Cross Street Windows
- Transfer to Capital 2016/2017
 - Classroom A/C and electrical upgrade
 - **Status** -Drawings complete filing with SED
- Facility line in budget
 - Cornice painting
 - Cupola repair
 - **Status**- Work not started, will coordinate with Window work

Middle School

- Facility line in budget
 - Bus Loop
 - **Status**- Bid award July 21
 - Hopeful work will be completed by start of school
 - Fab lab
 - **Status** - Work has begun
 - Summer school classroom air conditioning
 - **Status** - 6 rooms complete, electric and compressor completed for 6 additional future rooms

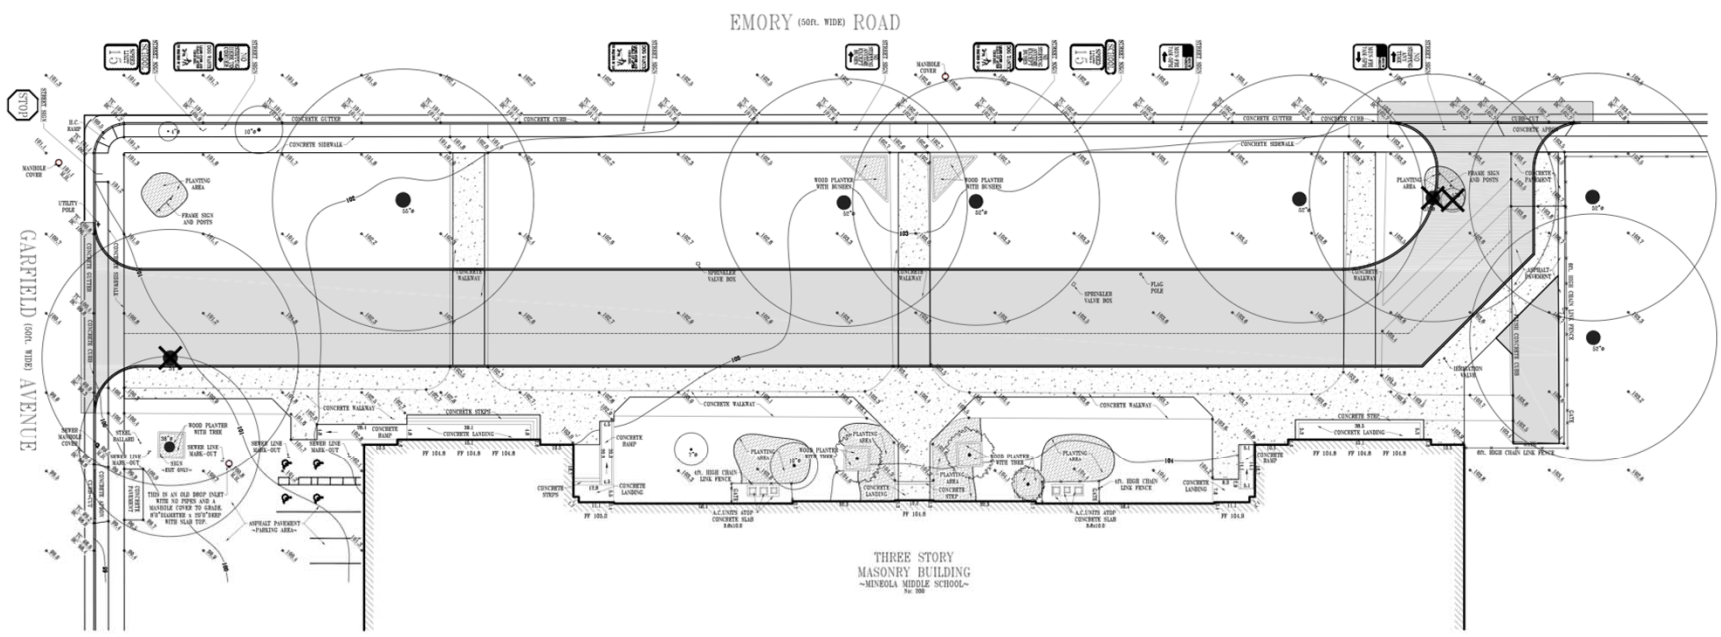

MINEOLA MIDDLE SCHOOL NEW BUS LOOP




MS Typical A/C unit



Room 211 conversion into
1 classroom


MS Fab Lab

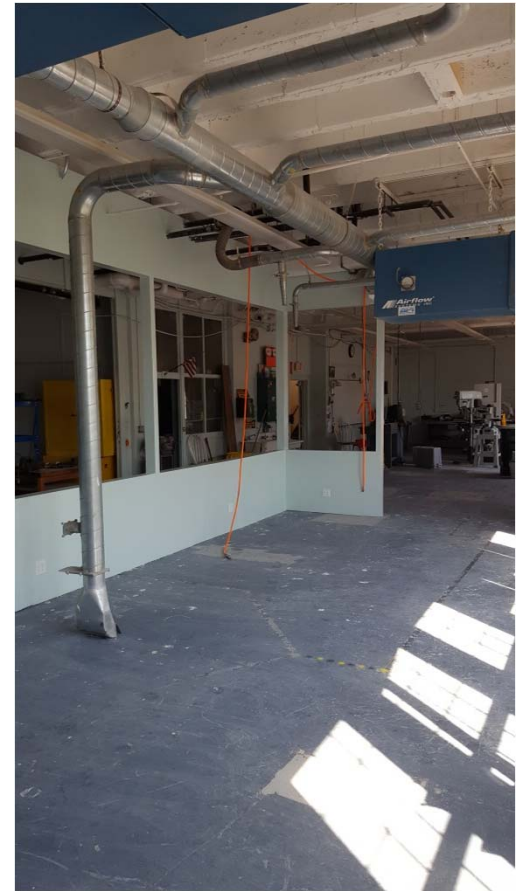


High School

- Capital Reserve Project (November 2015)
 - Track, field, Lobby ceiling
 - **Status**- track and field on schedule, Lobby framed and waiting for light fixtures
- Transfer to Capital 2016/2017
 - Renovate and construct 3 Music classrooms
 - **Status** - Demolition almost complete, pricing painting, floor scheduled, lights ordered. Waiting for final HVAC design and price
- Facility line in budget(s)
 - Fab Lab- **Status**
 - Demo and floors complete
 - Knee walls installed- soffit will begin July 25
 - Painting to begin July 25
 - Storefront in fabrication, HVAC ordered will install upon arrival
 - Baseball field concrete
 - **Status** - Have proposal from Land tek
 - Classroom renovations- rooms 134, 238, 240, old book room, ihub, offices
 - **Status**- all complete except 240
- Equipment
 - HS student lockers
 - **Status**- ordered and awaiting delivery- installation start 8/18


Track and Field

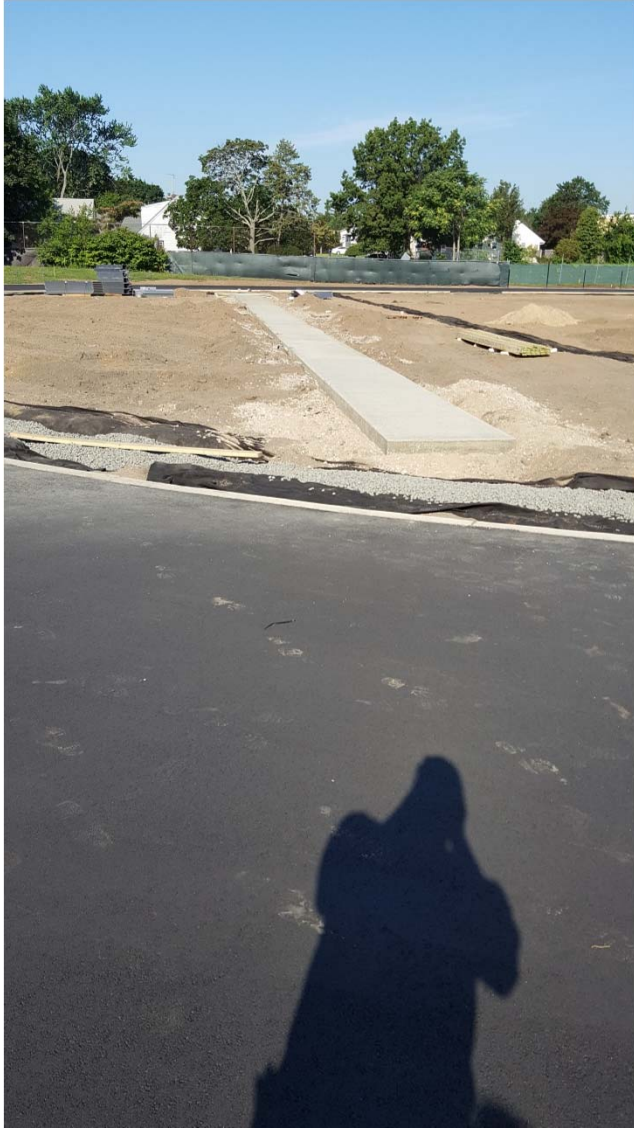



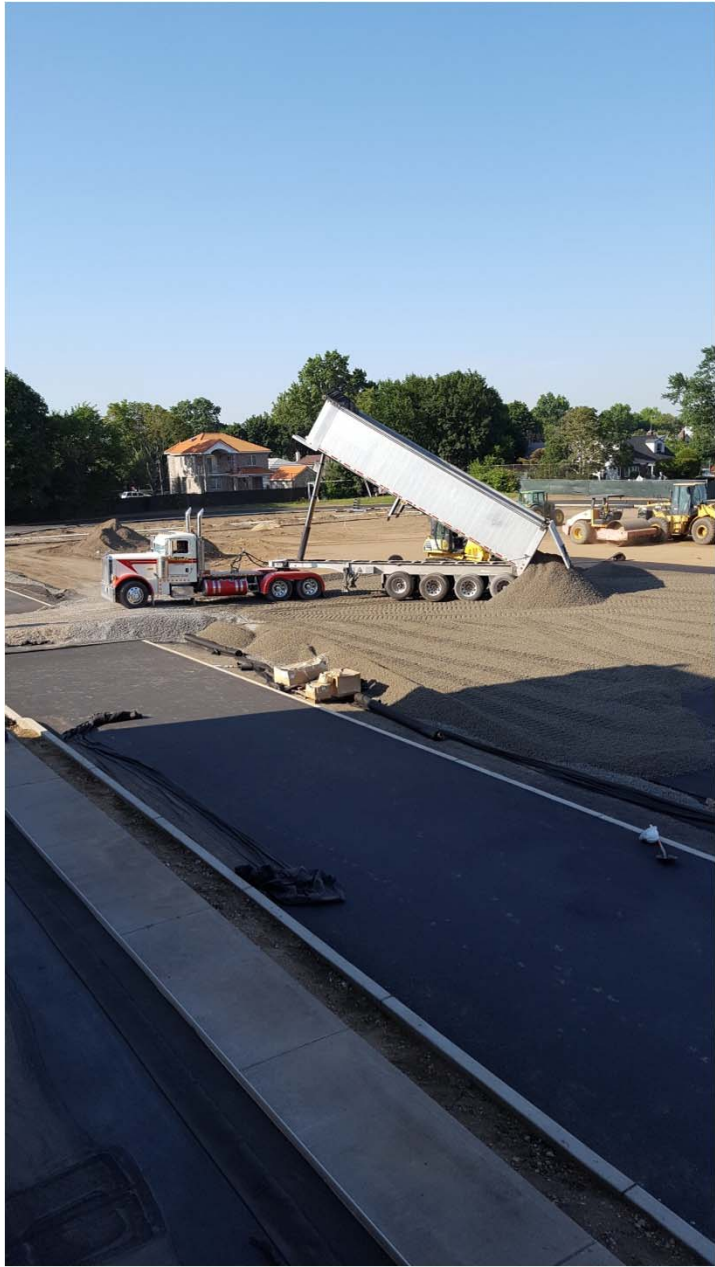



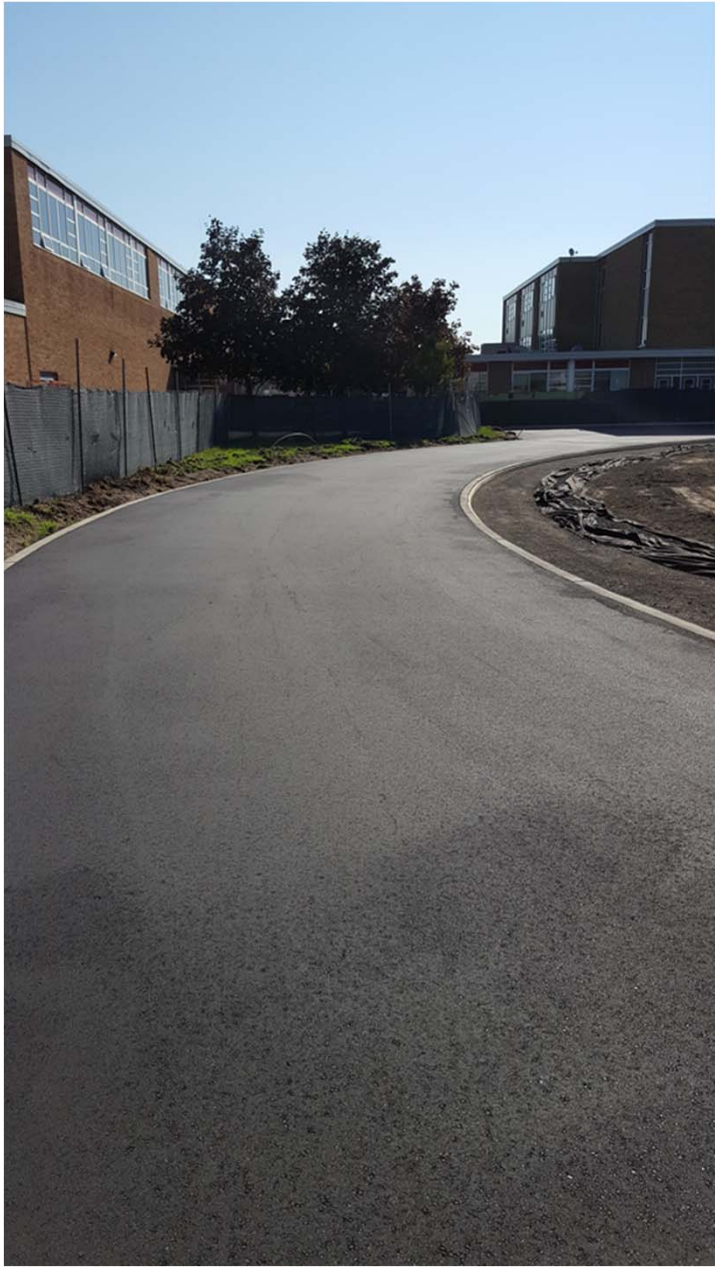

Fab Lab



