

# Long Range Facility Audit 2009-2019

Clovis Unified School District • August 2009



Century Elementary School





# Table of Contents

## Section Contents

- 1 Acknowledgements  
Executive Summary/Planning Guidelines
  - Project Scope
  - Project Timeline
  - Project Process
  - Project Recommendations
  - Cost Estimation
  - Final Deliverables
  - The Implementation of a 10-Year Facility Needs Master Plan
- 2 District-Wide Project Data
- 3 Site Requested Project List
  - Group 1: Other Schools/David E. Cook Center
  - Group 2: Buchanan Area
  - Group 3: Clovis North Area
  - Group 4: Clovis Area
  - Group 5: Clovis West Area
  - Group 6: Clovis East Area
- 4 Site Package





## Acknowledgements

HMC Architects submits the CUSD Facility Needs Assessment with acknowledgement to the District's Facility Division, Maintenance & Operations staff, Director of Construction & Engineering and over-all support from the office of the Assistant Superintendent, Facility Services. HMC would like to acknowledge the District Facility Audit Leadership team (listed below) for their support of the process to clarify and define the District building standards and their ongoing support of the facility audit process.

### **Board of Education**

Sandra A. Bengel  
Christopher Casado  
Brian D. Heryford  
Ginny Hovsepian  
Elizabeth J. Sandoval  
Scott Troescher  
Jim van Volkinburg, DDS

### **District Superintendent**

Terry Bradley, Ed.D, Superintendent

### **Steering Committee**

Don Ulrich, Assistant Superintendent, Facility Services  
Steve Ward, Associate Superintendent, Business Services  
John Poytress, Director of Plant Operations  
Stan Kawaguchi, Grounds Supervisor  
Brad Pawlowski, Maintenance Supervisor  
Chris Allen, Custodial Supervisor  
Bill Rice, Custodial Supervisor  
Robert Schram, Food Services Supervisor  
Rick Lawson, Director of Construction Services  
Dan Resciniti, Director of Technology Services  
Joe Bjerke, Director of Transportation

## Acknowledgements (cont'd)

HMC Architects and Harris Construction also recognize the following team of local consultants for their diligence in conducting a detailed assessment of the current facilities on 33 school sites and 12 District support facilities constructed prior to 2001 in the time schedule outlined by the District. In addition, all District facilities were assessed for the condition of technology. Their recommendations and insights are based on over 100 years of collective experience in public school construction.

Consultant	Company	Role
Scott Griffith	HMC Architects	Principal in Charge
Walt Byrd	HMC Architects	Project Manager
Jeff Berrios, Mandie Abels, Rick Sacksteder, Stanley Ng	HMC Architects	Building Conditions
Doug Reitz	Harris Construction	Cost Estimation & Scheduling
Tyler Arrigoni, John Fowler, Gil Galvan	OneInterface.net	Electrical & Technology
Gary Lindeman, David Oustad	Lawrence, Nye, Anderson	Mechanical & Plumbing
Sean Smith, Fred Wong	Blair, Church & Flynn	Site, Turf, Irrigation

Our team recognizes the extraordinary commitment of the Clovis community for supporting five local school bond measures, and the Clovis Unified School District Governing Board and Superintendent for their commitment to providing “world class” facilities for the students, staff and community. Faced with significant encroachments to the general fund, the CUSD Governing Board continues to prioritize funding for the construction of new schools, modernization and improvement of existing facilities, and Maintenance & Operation. Although our team has identified a significant amount of work for the District for over the next 10 years, every consultant commented on the excellent condition of the facilities targeted in this audit. Our team also recognizes the on-going efforts of the Plant Operations staff for their commitment to maintain all District facilities in excellent condition.

Last but not least, our team would like to express appreciation to HMC’s Ontario Office for their support of this project. In particular, we would like to recognize Amanda Ishak and Matt Endsley. Amanda and Matt proved to be an invaluable resource for our team in producing a final product that will serve as a roadmap to provide outstanding facilities for the students and staff of the Clovis Unified School District.



## Executive Summary/Planning Guidelines

The primary goal of the CUSD Long Range Facility Audit was to provide the same “standard” of learning environment for all students, and working environment for all employees. The Clovis Unified School District issued a Request for Proposals on October 12, 2008 to select a firm to conduct a Long Range Facility Needs Assessment. On December 1, 2008, the District selected HMC Architects, in partnership with Harris Construction, to clarify the District’s building and equipment standards, and to conduct a detailed facility needs assessment of existing facilities constructed prior to 2001. The condition of the technology infrastructure was assessed for all District sites, as well.

The objectives of the CUSD Facility Audit Request for Proposals were:

- Identify standards for the District’s infrastructure
- Assess District facilities constructed prior to 2001 against these standards
- Assess all District facilities against standards for technology infrastructure
- Identify , prioritize, and estimate costs for projects that will move all District facilities toward approved standards
- Identify projects into a 10 Year Facility Master Plan, with projects prioritized for 1-2 years, 3-5 years, and 6-10 years

## Project Scope

The scope of work for the CUSD Long Range Facility Audit included conducting a comprehensive audit of all current CUSD facilities constructed prior to 2001 (all sites were assessed for the condition of the technology infrastructure), including facilitating multiple meetings with site and District staff to clarify building and equipment standards for the following disciplines:

- Site Work
- Architectural/Building Conditions
- HVAC
- Plumbing
- Electrical
- Technology on all District facilities



## Project Timeline

### Phase 1: Completed by January 31, 2009


- Facilitate multiple meetings with District personnel to establish facility and equipment standards for disciplines identified

### Phase 2: Completed by May 31, 2009

- Conduct an assessment of all facilities constructed prior to 2001 and identify projects that will bring identified deficiencies up to approved District standards

### Phase 3: Completed by June 30, 2009

- Conduct a Governing Board workshop to update the Board and District Administration regarding the status of the CUSD Long Range Facility Audit
- Present a final report to District Leadership and CUSD Governing Board in both a written and electronic format

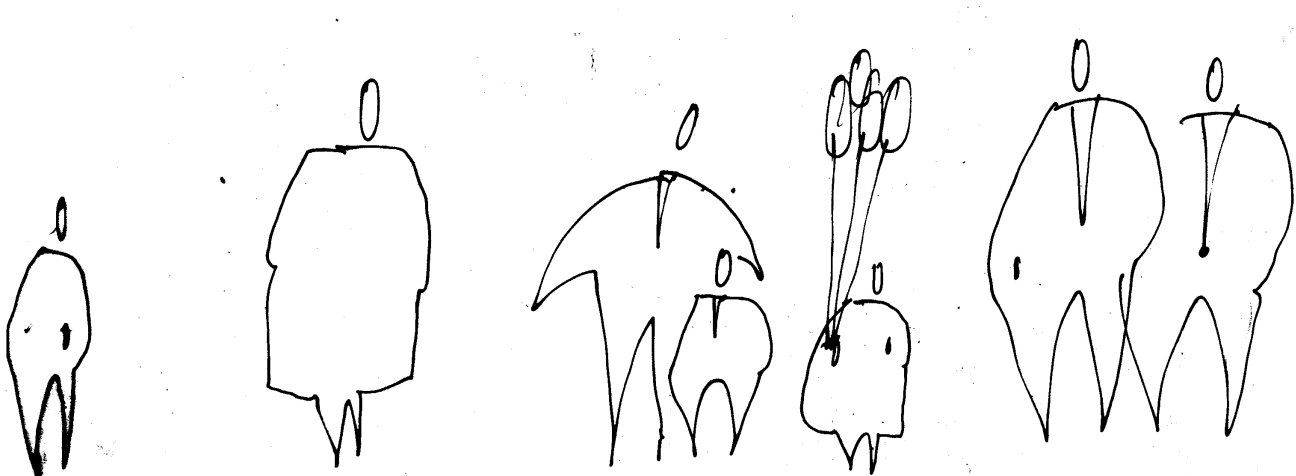





## Project Process

The following phases of work were established to address the scope of the CUSD Long Range Facility Audit within the timeframe established by the District. The expected outcome was to deliver a 10-Year Facility Master Plan, based on professional experience, and aligned with current and future funding opportunities.

### Phase 1: Meet with District Facility Leadership Team to clarify District Building Standards

- Task 1: Introduce Facility Needs Audit process to District Leadership through multiple District forums (Supt. Cabinet, Supt. Staff, Area Leadership meeting, District SART)
- Task 2: Review the following data related to the standard and condition of current facilities
- Elementary Education Specifications and Building Standards
  - District maintenance records
  - 10-year deferred maintenance program
  - 10-year District Facilities Master Plan
- Task 3: Meet with District Facility Leadership Team
- Scheduled milestones for the project
  - Clarify educational program goals and District Strategic Plan
  - Clarify the program for District Support Facilities
  - Establish sustainability goals and green practices for the project
  - Clarify equity standards and community expectations for each school
  - Establish District Building & Equipment Standards
- Task 4: Meet with site Principals and designated District staff of targeted sites:
- The facility audit process and purpose
  - Schedules and tasks
  - Site/facility self-assessment Zoomerang model
  - Clarify difference between District maintenance projects and facility audit projects

### Phase 2: Comprehensive Assessment of Facilities to identify deficiencies to District Standards

- Task 1: Project Monitoring Schedule
- Establish milestone meetings to include:
    - Site kick-off meetings
    - Site self-assessment schedule
    - Site visitations
    - Summery schedule with site staff
  - Conduct "mock" facility audit of elementary, secondary and support site
    - Train consultants for consistency
    - Establish common check lists for consultant to report findings from site visits
    - Provide results of site self-assessment surveys to consultants prior to visitation of the sites
  - Create and distribute a Site-Self Assessment Tool for the Principal and the Plant Supervisors to complete prior to consultant visits to sites
    - The Principal survey focused on how the facilities on their sites are addressing the following District Aims:
      - Maximizing Student Achievement
      - Ensuring a safe and positive learning environmentPrincipals and Directors were also asked to prioritize up to three facility projects on their campus
    - The Maintenance & Operations Survey focused on how the facilities are addressing the

## Project Process (cont'd)

following District Aim:

Operating with increasing efficiency and effectiveness

- Conduct facility audit to evaluate condition, and relationship to District Standards for each building
  - Consultants submit visitation schedules for site review
  - Site custodial staff and District maintenance staff available as needed to assist the audit team
- Conduct regular “milestone” meetings with consultants at the conclusion of each group of site visitations
  - Site observation checklist are submitted to Harris Construction for cost estimating, escalated to time of construction
- Consultants complete a summary report of findings, including, but not limited to, the following:
  - Itemized and detailed list of equipment condition, replacement schedule, infrastructure upgrades, modernizations/facility improvements to bring all sites into compliance with current accessibility, building codes, District educational specs, and/or standards sorted by site and by building
  - Make recommendations for future projects: 1-2 years, 3-5 years and 6-10 years
  - Project scope and schedule of work
  - Estimate costs to the date of construction for each project

### Phase 3: Final Deliverable for the District Facility Assessment Projects

- Task 1: Prepare milestone meeting report for the District Board Sub Committee
- Task 2: Prepare final deliverable document for Principals, Facility & Plant Op Departments, Governing Board, and Superintendent
- Facility Master Plan sorted by site which includes replacement and repair schedules
  - Projects sorted by Energy, Deferred Maintenance, Health & Safety, and ADA
  - Prioritize projects for the next 1-2 year, 3-5 years and 6-10 years
  - Escalate cost of each project to date of construction
- Task 3: Present findings and “draft” deliverable to the Governing Board
- Schedule a Board Workshop to present findings
- Task 4: Final Deliverable
- Governing Board to receive summary report of findings, including identified projects (including cost estimates) for all sites
  - The District Facility Leadership Team to receive a detailed summary of findings, including identified projects (included cost estimates) for all sites in a written and electronic format
    - The District will have ability to adjust and manipulate the database to respond to changing conditions within the District.
  - Site Principals/directors will receive a summary report of findings and projects for their school/ District site (including cost estimates)
- Task 5: Implementation of the Long Range Facility Audit
- Update Elementary and Secondary Educational Specifications
  - Conceptual Design for projects based on educational specifications
  - Create an implementation schedule for identified projects



## Project Recommendations

District Administrators, Principals, and Directors were provided an opportunity to identify projects they believed would enhance the efficiency and effectiveness of the District Mission “to be a quality educational system, providing the opportunity for all students to reach their potential in mind, body and spirit.” A wide variety of projects were suggested by the District. Individual projects were evaluated by our team of consultants, based on the following criteria, to determine their feasibility and practicality for the District:

- Alignment to the approved District building standards and educational specifications
- Alignment to the current educational program need(s) requested with the project
- Feasibility of cost to the District (based on our opinion) and space availability on the site

Cost estimations were only done on projects that our consultants felt aligned to the components of our “decision-making” criteria. Only projects that were determined to be feasible and practical were included in the site narratives.

## Cost Estimation

Potential project costs were estimated according to the cost index at the time of construction. An inflation calculator was incorporated into the detailed Excel spreadsheets for each site. Costs were estimated using a baseline average for equipment, materials & labor, and should be considered “estimates”. An additional 25% was added to each project that includes the “fees” for testing, inspection, and architectural/engineering. These costs (are in addition to the project construction costs) will need to be considered when the District chooses to schedule the project.



## Final Deliverables

Results were presented to the District in various formats depending on the needs of the end user. Below is a summary of the contents for these reports.

### District Staff

Governing Board and District Superintendent

Office of Facility Services

Office of Maintenance and Operations

Site Principals

### CUSD Facility Audit Report

District overview, including a Power Point presentation

District summary, summary of all schools and support facilities (including supporting detailed spreadsheets and consultant checklists)

School Site Summary Report





## The Implementation of a 10-Year Facility Needs Master Plan

The CUSD Facility Needs Audit will provide the District access to a significant amount of data, information, and recommendations regarding the condition of District facilities constructed prior to 2001 (and the technology infrastructure for all facilities). The primary goal of the CUSD Facility Needs Assessment was to develop a long range plan to bring all District school facilities, and support facilities, up to current approved District building and equipment standards. How the District chooses to use this data, information and recommendations to guide their decision making process, will be critical to the success of this effort.

It is our recommended that the District consider the CUSD Facility Audit within the context of a long range (10-year) Facility Master Plan. A 10-Year Facility Master Plan should be flexible and adaptable to changing conditions within the District and community. We feel that it will be essential to base decisions on a well crafted set of Elementary and Secondary Educational Specifications.

Another critical factor to be considered by the District will be the availability of state and local funding. It is our recommendation that an open dialogue begin immediately with the community to illustrate the need to upgrade current facilities well in advance of a formal campaign for a bond measure.

Important components that we recommend the District to consider, is to fully implement the results of the Long Range Facility Audit, are the following:


1. A thorough review and update of the District's current Elementary and Secondary educational specifications and building standards to insure alignment to curriculum and instructional methodologies to appropriate space relationships requirements.
2. Development of a conceptual design master plan, based on the educational specifications, for each building modernization, addition and expansion. These conceptual diagrams should identify the size, configuration and location of new facilities and reconfiguration of existing facilities.
3. Review current funding sources and begin to develop strategies for a future bond campaign. Evaluate the potential community tolerance for future bond initiatives for CUSD.
4. Strategically create a project implementation schedule for future projects indentified in the 10-Year Facility Needs Assessment Master Plan. This schedule must be based on maximizing current and potential funding sources.





## District-Wide Project Data

### District Summary

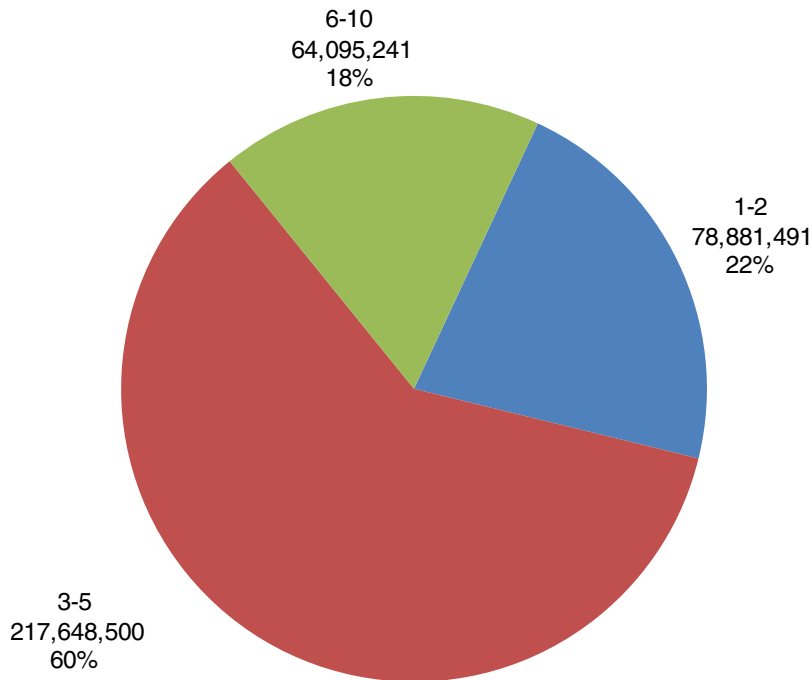


### Total District Needs Assessment





Summary by Area	Total
Group 1 - David E. Cook Center	50,304,840
Group 2 - Buchanan Area	77,683,445
Group 3 - Clovis North Area	17,534,207
Group 4 - Clovis Area	91,537,174
Group 5 - Clovis West Area	74,897,993
Group 6 - Clovis East Area	48,667,574
<b>Total</b>	<b>\$ 360,625,232</b>



## Breakdown by Project Category

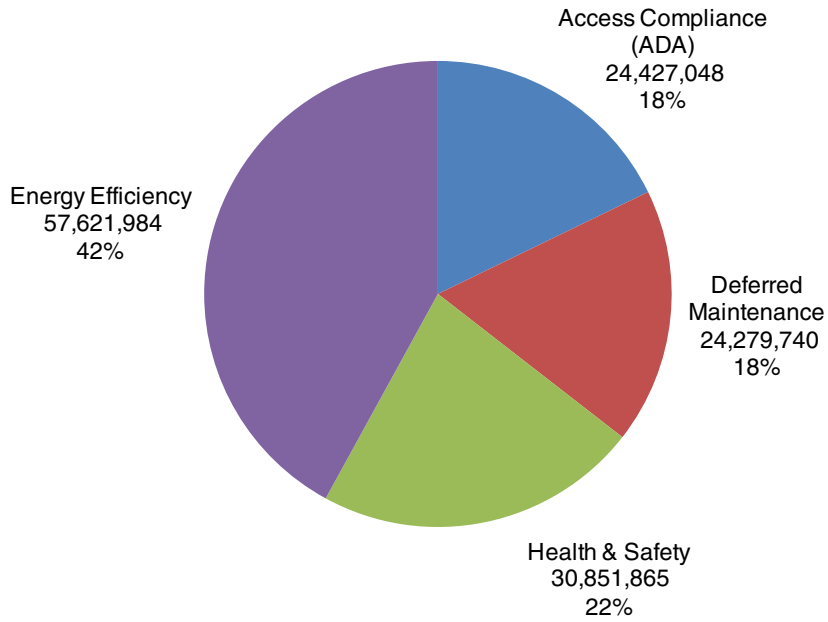


**TOTAL: \$137,180,638**

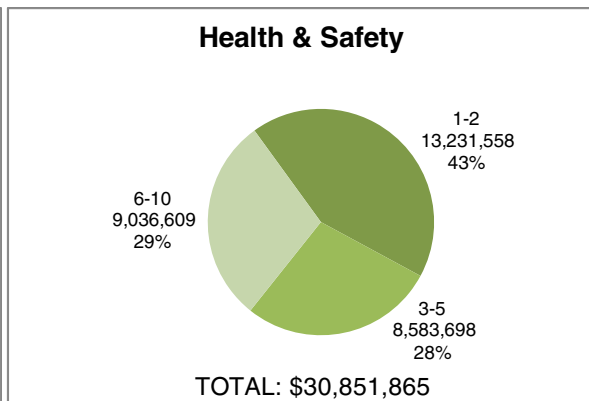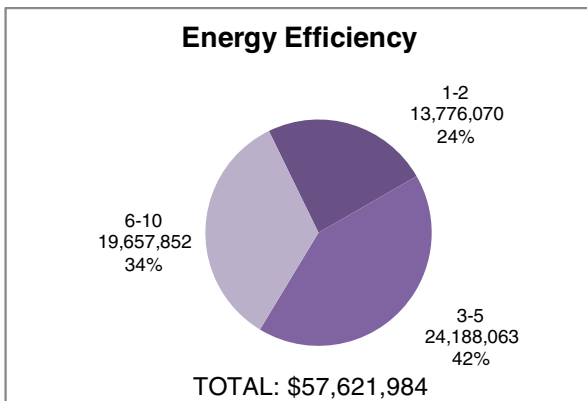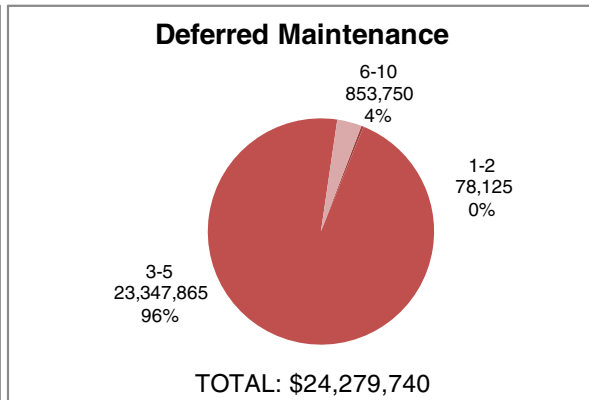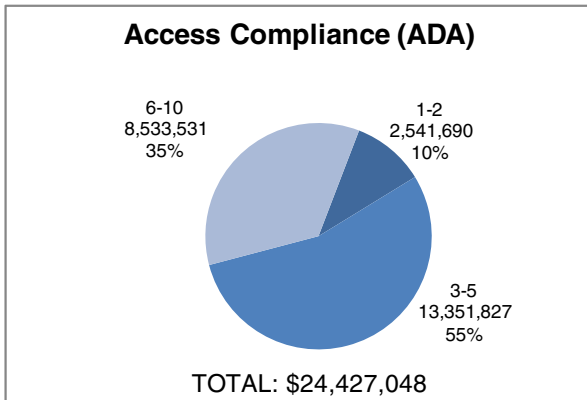





### Total by Discipline

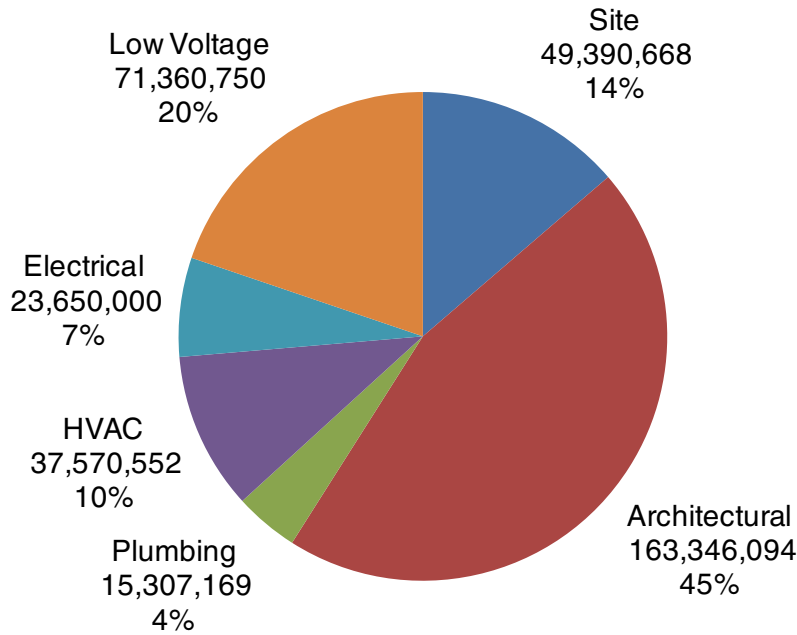







**TOTAL: \$360,625,232**

### Total District-Wide Needs Assessment

Summary by Discipline	1-2	3-5	6-10	TOTAL BY PROJECT CATEGORY
Site	13,085,930	20,967,763	15,336,975	49,390,668
Architectural	58,125	163,287,969	-	163,346,094
Plumbing	747,078	2,580,297	11,979,794	15,307,169
HVAC	9,138,608	14,504,597	13,927,347	37,570,552
Electrical	9,400,000	6,832,500	7,417,500	23,650,000
Low Voltage	46,451,750	9,475,375	15,433,625	71,360,750
<b>Total</b>	<b>\$ 78,881,491</b>	<b>\$ 217,648,500</b>	<b>\$ 64,095,241</b>	<b>\$ 360,625,232</b>




## Breakdown by Discipline

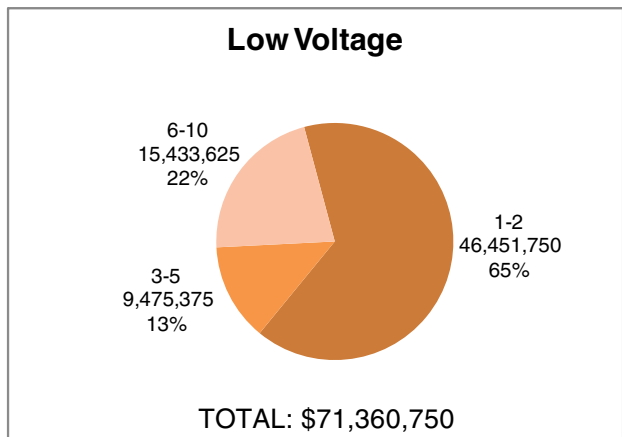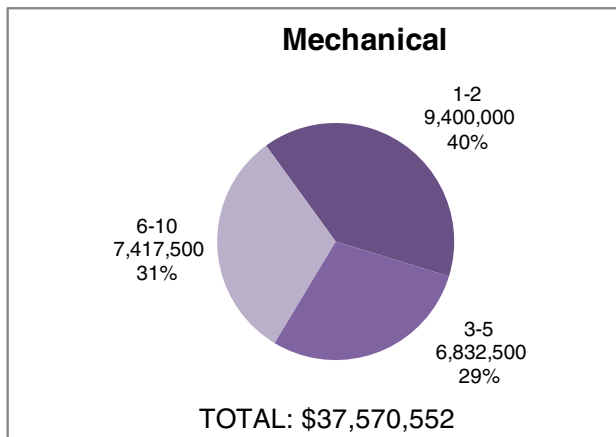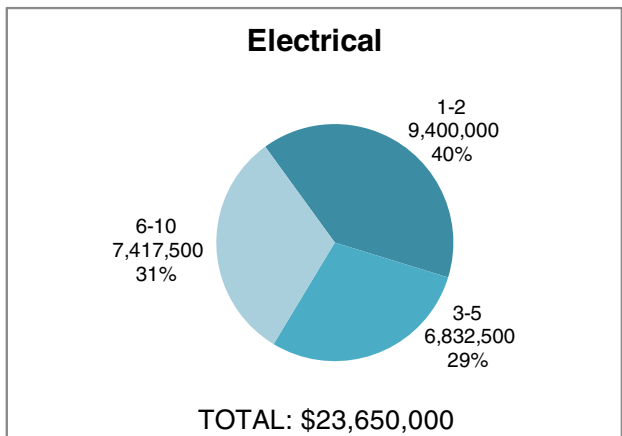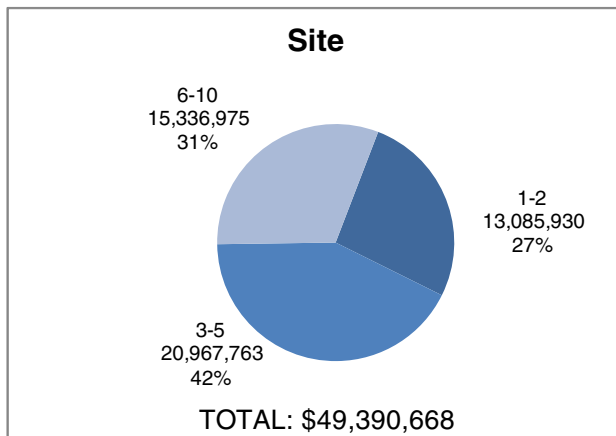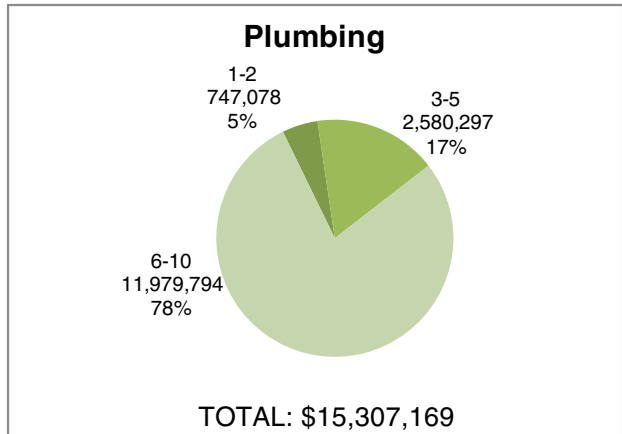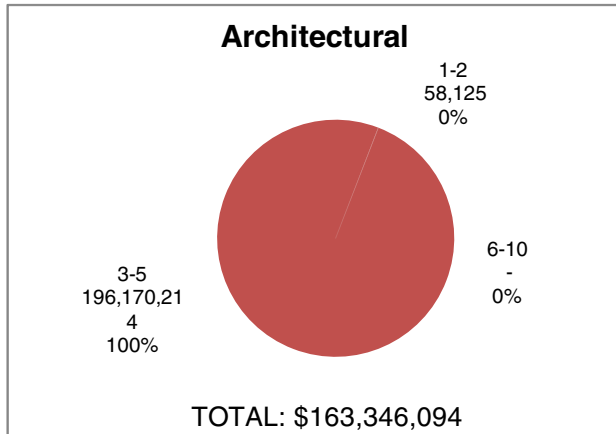




## Total by High School Attendance Area

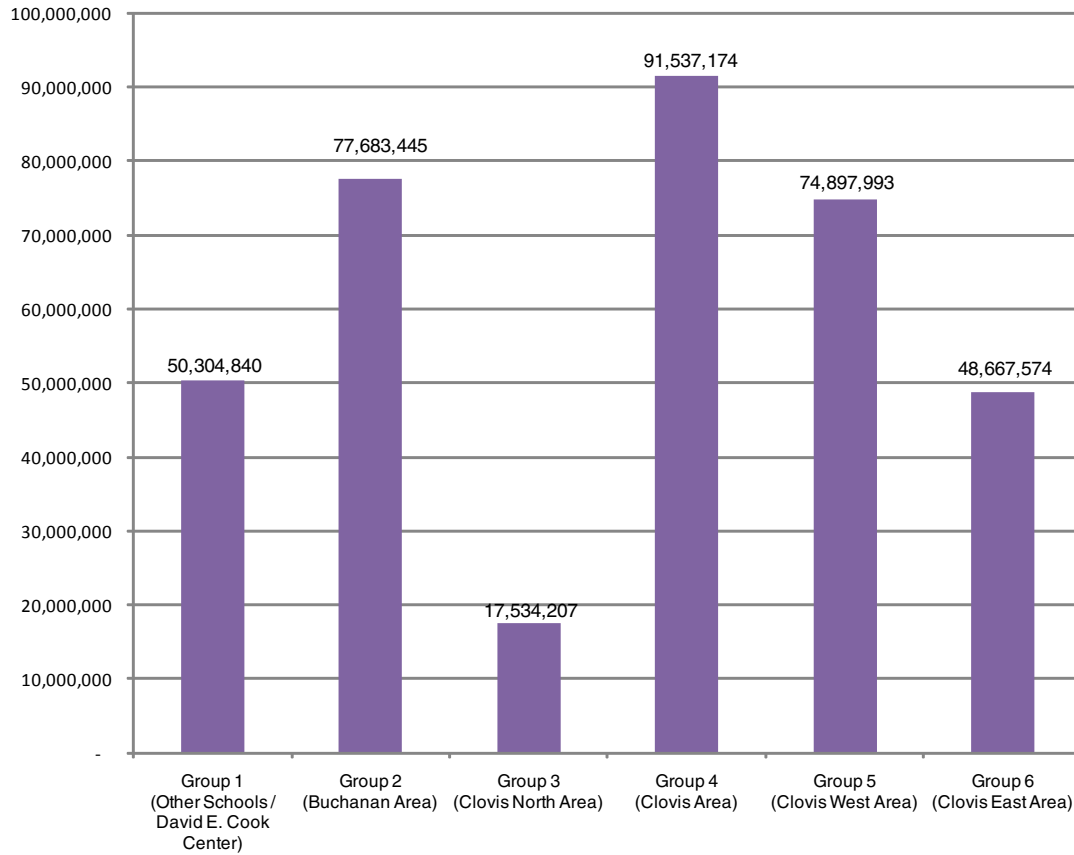

## Summary by Year of Construction

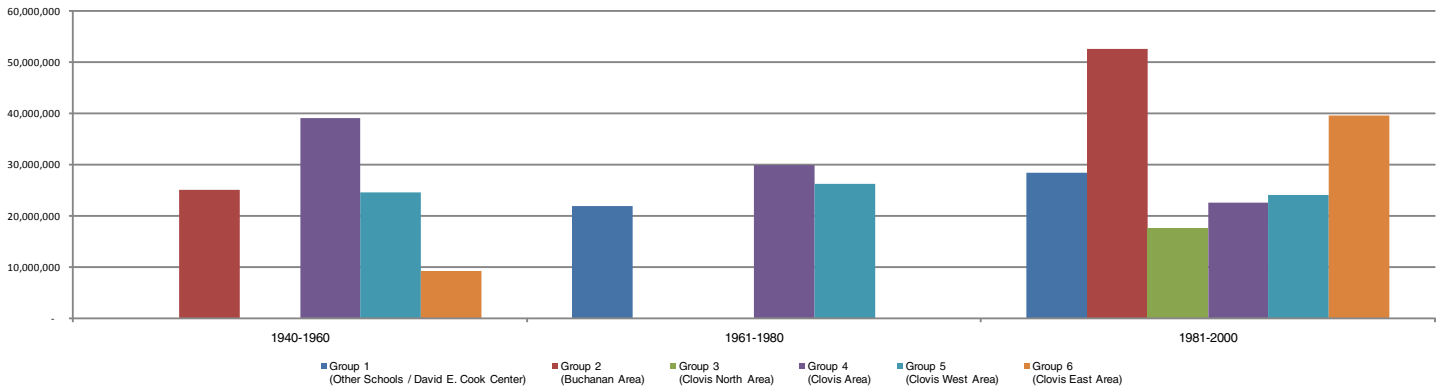



## District Wide Summary

School	1-2	3-5	6-10	TOTALS
Alta Sierra Intermediate School	2,496,910	5,216,060	2,096,841	9,809,811
Buchanan High School	2,186,412	21,113,939	6,053,820	29,354,171
Bud Rank Elementary School	110,000	0	263,125	373,125
Cedarwood Elementary School	1,436,885	2,494,889	600,128	4,531,902
Center for Advanced Research and Technology	1,196,649	223,846	3,290,386	4,710,881
Century Elementary School	1,417,335	2,656,039	1,667,101	5,740,475
Clark Intermediate School	2,474,515	11,935,481	3,538,113	17,948,109
Clovis Adult School	932,248	1,147,288	771,922	2,851,457
Clovis East High School	2,314,387	7,211,415	3,167,906	12,693,708
Clovis Elementary School	1,100,364	1,428,374	1,369,444	3,898,181
Clovis High School	2,410,497	15,979,777	6,308,134	24,698,408
Clovis North Educational Complex	16,250	0	0	16,250
Clovis West High School	3,061,024	8,037,810	3,922,954	15,021,788
Cole Elementary School	2,028,375	6,622,411	618,425	9,269,211
Community Day School	993,923	92,800	324,500	1,411,223
Copper Hills Elementary School	1,129,439	3,332,618	866,839	5,328,896
David E. Cook Center	4,113,934	10,129,830	2,608,958	16,852,721
Dry Creek Elementary School	2,934,689	3,401,961	861,266	7,197,916
Fancher Creek Elementary School	2,719,828	3,640,398	505,943	6,866,169
Fort Washington Elementary School	1,384,638	2,223,079	817,482	4,425,198
Freedom Elementary School	928,750	238,125	786,250	1,953,125
Fugman Elementary School	457,500	168,750	1,521,875	2,148,125
Garfield Elementary School	1,732,454	3,540,405	1,246,270	6,519,130
Gateway/Enterprise Alternative Education	568,218	3,035,519	1,460,165	5,063,902
Gettysburg Elementary School	2,631,511	5,551,824	982,827	9,166,161
Jefferson Elementary School	2,230,678	3,693,616	637,967	6,562,261
Kastner Intermediate School	1,828,375	7,082,309	2,336,927	11,247,611
Liberty Elementary School	2,189,887	4,008,284	337,368	6,535,539
Lincoln Elementary School	1,972,780	2,832,691	969,173	5,774,643
Maple Creek Elementary School	1,166,640	3,864,558	1,131,446	6,162,644
Mickey Cox Elementary School	1,444,861	3,077,500	725,055	5,247,416
Miramonte Elementary School	1,473,484	4,932,677	1,105,791	7,511,951
Mountain View Elementary School	2,203,822	4,700,859	624,754	7,529,436
Nelson Elementary School	2,330,241	2,987,061	517,735	5,835,037
Pinedale Elementary School	1,601,134	11,778,223	973,842	14,353,199
Reagan Elementary School	72,500	0	291,875	364,375
Red Bank Elementary School	1,999,173	2,079,408	888,234	4,966,814
Reyburn Intermediate School	1,609,284	5,748,866	2,748,988	10,107,138
Riverview Elementary School	864,000	298,125	976,250	2,138,375



## District Wide Summary

School	1-2	3-5	6-10	TOTALS
Sierra Outdoor School	802,875	18,460,531	151,250	19,414,656
Sierra Vista Elementary School	2,254,104	5,064,534	544,542	7,863,179
Tarpey Elementary School	2,216,081	5,631,262	790,013	8,637,355
Temperance-Kutner Elementary School	2,858,873	5,295,594	1,016,641	9,171,108
Valley Oak Elementary School	2,597,333	2,702,636	242,364	5,542,333
Weldon Elementary School	2,337,383	3,930,881	386,479	6,654,743
Woods Elementary School	51,250	56,250	1,047,875	1,155,375
Total:	\$ 78,881,491	\$ 217,648,500	\$ 64,095,241	\$ 360,625,232



# Site Requested Project List

(as submitted by site Principals)

## Group 1: Other Schools/David E. Cook Center

### Clovis Adult School

- None

### Center for Advanced Research and Technology

- HVAC system needs to be analyzed and repaired to assure a comfortable temperature for student learning. Some rooms exceed 85 degrees on a regular basis
- Replace locks on classroom doors to give teachers capability to lock from inside in the event of threat
- Repair/replace outside security cameras

### Gateway/Enterprise Alternative Education

- None

### Sierra Outdoor School

- Upper classroom building modernization
- Lower classroom building modernization
- New Gymnasium
- Irrigation to ball field
- Bus loading and unloading area
- Maintenance and Transportation Building
- Amphitheater stage

### Maintenance and Transportation Building

- Additional office space in the maintenance/transportation building
- Install restroom upstairs in work control area
- Push fence in north parking lot towards Herndon: redevelop parking lot
- Additional T-shed in outside storage area

### District Office West

- Landscape face-lift

### District Office East

- None

### Grounds Building

- Additional grounds building north of the existing grounds building: bays for storage
- Move mechanics shop to new building
- Add concrete and landscaping between Professional Development Building and warehouse

### Security and Attendance Building

- None

### Warehouse and Graphic Arts Building

- None

### District Services Building

- None

### Construction Services Building

- None



## Group 2: Buchanan Area

### Century Elementary School

- Rain gutters added to buildings
- Fix drainage problems around school
- Gates on Kindergarten parking lot to prevent people from driving on campus during off hours
- Review of main parking lot and bus loading zone
- Upgrade planter areas

### Cole Elementary School

- Technology Infrastructure
- New Multipurpose Room/Cafeteria/Teacher Lounge
- New Administrative office, reception and office staff area

### Dry Creek Elementary School

- Construction of a new academic building to house all 4-6 grade classes, music, and special education
- Landscape upgrade

### Garfield Elementary School

- A new addition to our library
- Landscaping and concrete areas need to be renovated
- Remodeling of the front office
- Kindergarten storage upgrade

### Tarpey Elementary School

- Main office expansion/upgrade
- Landscape upgrade

### Woods Elementary School

- None

### Alta Sierra Intermediate School

- Library demo kiosk
- Phone systems tech infrastructure
- Landscaping: hills planter flatten mounds

### Buchanan High School

- Heating and cooling system needs to be fixed
- Need a new counseling center
- Need a new bathroom facility at the pool

## Group 3: Clovis North Area

### Bud Rank Elementary School

- None

### Copper Hills Elementary School

- Extend student drop off zone

### Fugman Elementary School

- None

### Mountain View Elementary School

- HVAC upgrade

### Riverview Elementary School

- None

### Granite Ridge Intermediate School

- None

### Clovis North High School

- None



# Site Requested Project List (cont'd)

(as submitted by site Principals)

## Group 4: Clovis Area

### Cedarwood Elementary School

- Add dry wells on #2 and #3 baseball fields (very poor drainage)

### Clovis Elementary School

- Have bollards placed throughout the campus so people would not drive on the campus
- Have more signage and red painted curbs for entire frontage road that goes through the campus
- Area, lighting, and sound
- Multipurpose Room window coverings

### Mickey Cox Elementary School

- Lighting: improved in kindergarten classrooms, cafeteria and amphitheatre areas
- Air condition corrections: students get irritable and act out when the temperature gets too high in the classrooms and library

### Gettysburg Elementary School

- We would love to have a new snack bar, like newer schools have, out by our ball fields. This would also allow us some much needed storage space

### Jefferson Elementary School

- Public address/bell system
- Air conditioning both chiller and boiler need to be replaced
- Cameras need to be repaired to work correctly

### Red Bank Elementary School

- HVAC
- Teacher workroom expansion
- Access to greater technology in the classroom (projector, wireless, etc.)

### Sierra Vista Elementary School

- Library expansion
- Moderization of Multipurpose Room
- AC/Heating system replaced
- Cement upgrade and repair

### Weldon Elementary School

- Concrete project in front of A wing and blacktop
- Classroom technology renovation (electrical access, ceiling mounts for LCD, pull down screens)
- Multipurpose Room/Kitchen renovation

### Clark Intermediate School

- New gym floor (scheduled: added athletic facilities, field space: Rodeo Grounds)
- Technology that would allow classrooms to have video capabilities
- Amphitheater landscape upgrade
- Room for stagecraft and storage for the MET
- Landscaping, irrigation, and playfield improvements

### Clovis High School

- The lockers in the girls locker room need to be replaced from 1969 to provide larger lockers for students to store their backpacks in during PE class to prevent thefts including enough lockers for each student
- Modernization of facilities to have all classrooms have LCD mounts and wiring in the ceiling, computers labs, field houses, band and folklorico practice rooms, etc.





## Group 5: Clovis West Area

### Fort Washington Elementary School

- None

### Liberty Elementary School

- Renovate the main office/library
- Get a new AC/Heating system
- Additional areas for teacher collaboration and storage

### Lincoln Elementary School

- New restrooms adjacent to the playground.  
Currently the only restrooms close by are in the snack bar area and face away from supervision
- Walkway-cement work: cement curbs for flower beds, cement work for raised planter boxes
- Regrading grass: drainage issues

### Maple Creek Elementary School

- Air conditioning and heating unit replaced
- Fire alarm system-heat sensors
- Traffic calming devices and speed bumps in parking lot

### Nelson Elementary School

- Multipurpose Room modernizing
- HVAC upgrades
- Updating of paint/landscaping
- Technology infrastructure

### Pinedale Elementary School

- Multipurpose Room modernizing
- Library Media Center
- Classroom space and design to meet the vision of our schools
- Improvement in technology in the buildings so that it supports our vision, and improvement in the cooling and heating systems
- Remodel Classroom

### Valley Oak Elementary School

- Window replacement

### Kastner Intermediate School

- Need upgrade technology labs
- Locker room lockers sorely need to be replaced
- Chiller and air handler in Multipurpose Room/ Bandroom always down
- Replace gym bleachers as wood bleachers are a safety hazard
- Need to retrofit the woodshop with safer equipment
- Replace gymnasium bleachers

### Clovis West High School

- Camera Installation
- More fob systems for doors so access into A building by staff does not require the need to leave the doors unlocked
- Completion of appropriate counseling center



## Site Requested Project List (cont'd)

(as submitted by site Principals)

### Group 6: Clovis East Area

#### Fancher Creek Elementary School

- A new addition to our library
- Landscaping and concrete areas need to be renovated
- Remodeling of the front office

#### Freedom Elementary School

- None

#### Miramonte Elementary School

- Landscape upgrade
- Modernize main office

#### Reagan Elementary School

- None

#### Temperance-Kutner Elementary School

- Build a main office
- A new AC/Heating system
- security alarm system for entire school
- Technology infrastructure

#### Reyburn Intermediate School

- HVAC upgrades
- Bell/alarm sensors
- Water main cracks

#### Clovis East High School

- Athletic office modernization
- New restrooms for baseball stadium



## Site Areas

### **Group 1: Other Schools/David E. Cook Center**

- Clovis Adult School
- Center for Advanced Research and Technology
- Gateway/Enterprise Alternative Education
- Community Day School
- Sierra Outdoor School
- Maintenance and Transportation Building
- District Office West
- District Office East
- Grounds Building
- Security and Attendance Building
- Warehouse and Graphic Arts Building
- District Services Building
- Construction Services Building
- Professional Development Building

### **Group 2: Buchanan Area**

- Century Elementary School
- Cole Elementary School
- Dry Creek Elementary School
- Garfield Elementary School
- Tarpey Elementary School
- Woods Elementary School
- Alta Sierra Intermediate School
- Buchanan High School

### **Group 3: Clovis North Area**

- Bud Rank Elementary School
- Copper Hills Elementary School
- Fugman Elementary School
- Mountain View Elementary School
- Riverview Elementary School
- Clovis North Educational Center

### **Group 4: Clovis Area**

- Cedarwood Elementary School
- Clovis Elementary School
- Mickey Cox Elementary School
- Gettysburg Elementary School
- Jefferson Elementary School
- Red Bank Elementary School
- Sierra Vista Elementary School
- Weldon Elementary School
- Clark Intermediate School
- Clovis High School

### **Group 5: Clovis West Area**

- Fort Washington Elementary School
- Liberty Elementary School
- Lincoln Elementary School
- Maple Creek Elementary School
- Nelson Elementary School
- Pinedale Elementary School
- Valley Oak Elementary School
- Kastner Intermediate School
- Clovis West High School

### **Group 6: Clovis East Area**

- Fancher Creek Elementary School
- Freedom Elementary School
- Miramonte Elementary School
- Reagan Elementary School
- Temperance-Kutner Elementary School
- Reyburn Intermediate School
- Clovis East High School





# Century Elementary School

965 N. Sunnyside, Clovis, CA 93611 • t. 559-327-8400, f. 559-327-8490



## General Information

<b>Grade Level Configuration:</b>	K-6
<b>Enrollment Capacity:</b>	725
<b>Site Acreage:</b>	15
<b>Total Plan Square Footage:</b>	47,310

**Overview:** Century Elementary School was built in 2000. Century Elementary has 23 permanent classrooms and 13 portable classrooms to accommodate a student body of 725. Along with an administration building, library media center, multi-purpose room, snack bar and restrooms the facilities adequately support the instructional program. Century Elementary has many athletic fields that are used for recess, sports, and other co-curricular activities during and outside the school day. Various community groups utilize the facilities and playfields outside the school day. At this time the school is currently operating at capacity.

# Year Built/Renovated/Modernized

Based on available drawings and discussions with District maintenance personnel, we obtained the following information regarding year constructed and Division of the State Architect (DSA) approval for campus construction projects.

**Opened:** 2000  
**Architect:** SOMAM

Building/Rooms:	DSA Application Number:	Approval Date:	<u>MODERNIZATION ELIGIBILITY</u>	
			25 Years + 12 Months:	50 Years + 12 Months:
All	64506	11/26/1997	11/26/2023	11/26/2048

## Site Plan Legend

-  Classroom Building
-  Kindergarten
-  Multipurpose Room
-  Snack Bar
-  Administration
-  Library/Media Center
-  Locker Room
-  Wrestling/Weights
-  Restroom
-  Gymnasium
-  Shop Building
-  Maintenance
-  Cluster Office
-  Storage Building
-  Concert Hall
-  Field House
-  Pool Office
-  Portables
-  Large Gym
-  Small Gym





# Site Plan



# Civil Engineering

## ADA Compliance

Observations: The concrete condition is fair. There are many locations of cracking and trip hazards. The curb ramps do not meet ADA requirements. The accessible stall signage and striping require minor changes. ADA detectable warning surface is required in various locations. Storm drain inlet grates do not meet ADA requirements for maximum grate openings. Walk gates do not meet ADA requirements. Some drinking fountains do not meet ADA requirements.

Recommendations: Reconstruct concrete improvements to eliminate trip hazards and comply with ADA curb ramp requirements. • Add accessible stall signage and striping as required. • Add ADA detectable warning surface at various locations. • Replace storm drain inlet grates in accessible paths of travel with ADA compliant grates. • Replace walk gates with ADA compliant gate hardware. • Replace drinking fountains with ADA compliant drinking fountains.

## Site Drainage

Observations: The storm drain system is in good working condition, but there is evidence of standing water in a few site planters.

Recommendations: Add additional storm drain inlets in planter areas to prevent standing water.

## Transportation Facilities

Observations: There are 68 standard parking stalls on the campus - 32 short of the District Standard of 100. There are also 4 accessible parking stalls – meeting the ADA requirements. Bus loading zone length complies with District Standards. Parent drop-off zone length complies with District Standards. There are bicycle racks for 75 bicycles – meeting the District Standards.

Recommendations: Although the site provides 32 fewer stalls than District Standard of 100, there is off-site parking available along the school frontage that may offset this deficit. The District should consider the amount and availability of off-site street parking in evaluating whether or not to provide additional on-site parking.

## Athletic Facilities

Observations: The 3 backstops do not have ADA compliant field access. 1 of the backstops has a grass infield. Playfields and playcourts meet District Standards. There is 1 long jump pit.

Recommendations: Reconstruct backstop field access to meet ADA requirements. • Skin 1 grass infield.

## Landscape

Observations: There are a few locations of bare planters. There are a few locations of bare turf. Weed control is good. There is a concrete amphitheatre on campus.

Recommendations: Add shrubs, ground cover, and trees to bare planters. • Replace turf in bare areas. • Eradicate weeds as required.

## Irrigation System

Observations: The irrigation system is 10 years old and is in good working condition. Minor irrigation repairs are required in various planter areas.

Recommendations: Repair irrigation in various planter areas as required.





## Architectural

### Administration Building

Observations: The building functions for its intended use and adequately provides for quality spaces.

Recommendations: Refer to cost sheet for minor recommendations.

### Library Media Center

Observations: The building functions for its intended use and adequately provides for a quality space, however the reading and stack areas are less than the district standards. The storage area is also under sized and does not have a sink with counter space.

Recommendations: Identify the area shortfall and consider an addition to mitigate needed reading, stacks and storage area, as well as plumbing fixtures and casework. • Refer to cost sheet for minor recommendations.

### Multi-Purpose Building

Observations: The building functions for its intended use and adequately provides for quality spaces, except for the undersized custodial office and storage.

Recommendations: Provide an addition to the custodial area for additional work area and storage. • Refer to cost sheet for minor recommendations.

### Classroom Building C-a - C-e

Observations: The building functions for its intended use and adequately provides for quality spaces.

Recommendations: Refer to cost sheet for minor recommendations.

### Portable Classrooms

Observations: The buildings function for their intended use and adequately provides for a quality space.

Recommendations: Refer to cost sheet for minor recommendations.

### Snack Bar Building

Observations: The building functions for its intended use and adequately provides for a quality space.

Recommendations: Refer to cost sheet for minor recommendations.

# Plumbing Engineering

## Administration Building

Observations: Most plumbing fixtures meet the district standard. Most fixtures are ADA compliant. Most fixtures are in good condition.

Recommendations: No modernization is required before 6-10 years. • ADA retrofit is suggested.

## Multi-Purpose Building/Central Plant

Observations: Most plumbing fixtures meet the district standard. Most fixtures are ADA compliant. Most fixtures are in good condition.

Recommendations: No modernization is required before 6-10 years. • ADA retrofit is suggested.

## Classroom Building C-a

Observations: All plumbing fixtures meet the district standard. Most fixtures are ADA compliant. Most fixtures are in good condition.

Recommendations: No modernization is required before 6-10 years. • ADA retrofit is suggested.

## Classroom Building C-b

Observations: Most plumbing fixtures meet the district standard. Most fixtures are ADA compliant. Most fixtures are in good condition.

Recommendations: No modernization is required before 6-10 years. • ADA retrofit is suggested.

## Classroom Building C-c

Observations: All plumbing fixtures meet the district standard. Most fixtures are ADA compliant. Most fixtures are in good condition.

Recommendations: No modernization is required before 6-10 years. • ADA retrofit is suggested.

## Classroom Building C-d

Observations: All plumbing fixtures meet the district standard. Most fixtures are ADA compliant. Most fixtures are in good condition.

Recommendations: No modernization is required before 6-10 years. • ADA retrofit is suggested.

## Classroom Building C-e

Observations: All plumbing fixtures meet the district standard. Most fixtures are ADA compliant. Most fixtures are in good condition.

Recommendations: No modernization is required before 6-10 years. • ADA retrofit is suggested.

## Classroom Building C-f

Observations: All plumbing fixtures meet the district standard. Most fixtures are ADA compliant. Most fixtures are in good condition.

Recommendations: No modernization is required before 6-10 years. • ADA retrofit is suggested.



## Plumbing Engineering (cont'd)

### Snack Bar/Toilet Building

Observations: Most plumbing fixtures meet the standard. Most fixtures are ADA compliant. All fixtures are in good condition.

Recommendations: No modernization is required before 6-10 years. ADA retrofit is suggested.

### Site

Observations: A lack of building isolation valves and sewer backups.

Recommendations: Add isolation valves and cleanouts.

## HVAC

### Administration Building

Observations: The condensing units and furnaces units do not comply with the district standard. The library is served by air handlers from the central plant. All exhaust fans are operating. The data room does have separate cooling. The EMS is full DDC.

Recommendations: This building is energy efficient. • No other modernization is required before 6-10 years. • Replace or refurbish units at modernization.

### Multi-Purpose Building/Central Plant

Observations: The building uses air handlers and is served by the central plant. The chiller and boiler do not meet the district standard. Some exhaust fans are operating. The EMS is full DDC.

Recommendations: This building is energy efficient. No modernization is required before 6-10 years. • Energy use of the pumps and air handlers may benefit from the addition of VFDs. • Replace or refurbish units at modernization. • New chiller and boiler will increase energy efficiency.

### Classroom Building C-a

Observations: The classrooms use unit ventilators and are served by the central plant. The EMS is not full DDC.

Recommendations: This building is energy efficient. • No modernization is required before 6-10 years. • Add DDC controls. • Replace or refurbish units at modernization.

### Classroom Building C-b

Observations: The classrooms use unit ventilators and are served by the central plant. All exhaust fans operate. The EMS is not full DDC.

Recommendations: This building is energy efficient. No modernization is required before 6-10 years. • Add DDC controls. • Replace or refurbish units at modernization.

### Classroom Building C-c

Observations: The classrooms use unit ventilators and are served by the central plant. • The EMS is not full DDC.

## HVAC (cont'd)

Recommendations: This building is energy efficient. • No modernization is required before 6-10 years. • Add DDC controls. • Replace or refurbish units at modernization.

### Classroom Building C-d

Observations: The classrooms use unit ventilators and are served by the central plant. The EMS is not full DDC.

Recommendations: This building is energy efficient. • No modernization is required before 6-10 years. • Add DDC controls. • Replace or refurbish units at modernization.

### Classroom Building C-e

Observations: The classrooms use unit ventilators and are served by the central plant. The EMS is not full DDC.

Recommendations: This building is energy efficient. • No modernization is required before 6-10 years. • Add DDC controls. • Replace or refurbish units at modernization.

### Portable Classrooms

Observations: The heat pumps do not meet the district standard. All exhaust fans operate.

Recommendations: These buildings are not energy efficient. • No modernization is required before 6-10 years. • Energy use will benefit from the retrofit to high efficiency heat pumps and DDC control.

### Snack Bar/Toilet Building

Observations: The snack bar does not have air conditioning. It does not meet the district standard. All exhaust fans operate.

Recommendations: These buildings are not energy efficient. • No modernization is required before 3-5 years. • Energy use will benefit from the retrofit to high efficiency heat pumps and DDC control.



# Electrical Engineering

## Site Electrical Distribution System

Observation: The Century site electrical distribution system is in poor condition and is not compliant with current electrical codes.

Recommendation: Replace electrical panels and feeders.

## Site Electrical Lighting System

Observation: Parking lot lighting and exterior pathway lighting is poor condition and does not meet current electrical codes.

Recommendation: Replace parking lot lighting and pathway lighting. • Century is in need of surveillance lighting controls to provide adequate lighting coverage for the surveillance camera system.

## Electrical Distribution System

Observation: The electrical distribution system for each building at Century is in poor condition and is not compliant with current electrical codes.

Recommendation: Replace electrical panels and circuits.

## Electrical Lighting System

Observation: The electrical lighting system is in good condition with good coverage.

Recommendation: No work recommended.

## Site Theatrical Lighting System

Observation: The Century theatrical lighting system is in poor condition and is not compliant with District standards. Light fixtures are not energy efficient.

Recommendation: Replace light fixtures, wiring, controls, and electronics.

## Site Sound Reinforcement System

Observation: The sound reinforcement system is in poor condition and is not compliant with District and industry standards.

Recommendation: Replace loudspeakers, wiring, controls, and electronics.

# Low Voltage

## Site Fire Alarm System

Observation: The Fire Alarm system is in poor condition and is compliant with current District standards or electrical codes.

Recommendation: Replace fire alarm system, cabling, and devices.

## Site Telephone System

Observation: The telephone system at Century is in poor condition and does not meet the District standard. Telephone cabling does not comply with current industry standards and electrical codes.

Recommendation: Replace telephone system, cabling, and handsets.

## Site CATV System

Observation: The CATV system is in good condition and meets District standards.

Recommendation: No work recommended.

## Site Clock System

Observation: The current clock system at Century does not meet District standards.

Recommendation: Replace clock system and devices.

## Site Public Address System

Observation: The Century public address system does not comply with current District standards. Public Address cabling is in poor condition and is not compliant with current electrical codes.

Recommendation: Replace public address system, cabling, and devices.

## Site Camera Surveillance System

Observation: The camera surveillance system is in good condition, has adequate coverage, and meets current District standards.

Recommendation: No work recommended.

## Site Audio Visual System

There are approximately (29) locations at Century that do not have an audio visual system or the current system does not meet District standards.

Recommendation: Install projector, projection screen, loudspeaker, and audio visual controls for each location.

## Data System

Observation: The Century data system is not compliant with current District and industry standards. Data system spaces do not provide adequate room or cooling. Network cabling does not have the capabilities to run high speed networks as required by District standards. Telecom spaces do not have a District standard UPS for power backup.

Recommendation: (1) Data system space requires architectural improvements to meet District and industry standards.

- Approximately (4) new data system spaces are required.
- All network cabling should be replaced.
- Each data space requires a new UPS and cooling system.
- This site requires (1) environmentally controlled pedestal to contain data system electronics and terminations for portable buildings.



## Low Voltage (cont'd)

Project Request

Maintenance & Operations: "Upgrade electrical panels and wiring campus wide."  
Response: Accommodated in next modernization.

Maintenance & Operations: "Metal halide lighting."  
Response: Accommodated in next modernization.

Maintenance & Operations: "Replace low voltage wiring campus wide ."  
Response: Accommodated in next modernization.



## Summary by Discipline and Priority

Century Elementary School		1-2	3-5	6-10	TOTALS
Site		186,343	342,886	126,711	655,940
Architectural		0	1,510,108	0	1,510,108
Plumbing		3,225	11,288	238,050	252,563
HVAC		0	202,550	464,920	667,470
Electrical		226,000	0	146,000	372,000
Low Voltage		718,300	58,000	358,000	1,134,300
	Subtotals:	\$ 1,133,868	\$ 2,124,831	\$ 1,333,681	\$ 4,592,380
Contingency	5%	56,693	106,242	66,684	229,619
Haz Mat Abatement	5%	56,693	106,242	66,684	229,619
A/E Fees	10%	113,387	212,483	133,368	459,238
Testing and Inspections	5%	56,693	106,242	66,684	229,619
	Total:	\$ 1,417,335	\$ 2,656,039	\$ 1,667,101	\$ 5,740,475

An additional 25% was added to each project that includes the “fees” for testing, inspection, and architectural/engineering. These costs (are in addition to the project construction costs) will need to be considered when the District chooses to schedule the project.





## Projects by Discipline and Sub-Categories

Century Elementary School		TOTALS
<b>Site</b>		
Asphalt and Play Court Renovations		1,500
Transportation and Parking Lot Improvements		157,706
Site Plumbing Renovations		43,750
Site Drainage Improvements		14,875
Site Concrete, Ramps, Stairs, and ADA Improvements		168,986
Landscaping, Irrigation, and Play Field Improvements		428,608
Fencing and Gates Upgrades		4,500
<b>Architectural</b>		
Improve planter drainage		3,125
Replace and/or repair roofing, roof fences and fascia		271,875
Replace and/or add Play Area or Athletic Field facilities		15,875
Repair and/or replace window, door and hardware systems		14,531
Repair and/or replace interior wall finishes		29,500
Repair and/or replace floors and floor coverings		540,688
Repair and/or Replace casework		79,641
Paint interior and/or exterior walls		27,000
Expand and/or reconfigure Multipurpose building		265,563
Expand and/or reconfigure Library Media Center building		612,500
ADA Required upgrades		27,338
<b>Plumbing</b>		
Classroom Plumbing Replacement		169,656
Toilet Room Plumbing Replacement.		146,047
<b>HVAC</b>		
HVAC/Chiller Upgrade and/or Replacement		704,650
EMS Upgrade and/or Replacement		129,688
<b>Electrical</b>		
Exterior Power Distribution Energy Improvements		157,500
Building Lighting Efficiency Improvements		147,500
Exterior Lighting Efficiency Improvements		82,500
Building Power Distribution Energy Improvements		77,500
<b>Low Voltage</b>		
Exterior Lighting Efficiency Improvements		16,250
Technology System Improvements		1,245,375
Fire Alarm/Life Safety		156,250
Total	\$	5,740,475



## Summary by Location, Priority and Special Categories

Century Elementary School	1-2	3-5	6-10	H&S	DFM	ADA	EE
<b>Site</b>							
Site Plumbing Renovations	43,750	0	0				
Transportation and Parking Lot Improvements	206	0	157,500			•	
Site Drainage Improvements	14,875	0	0				
Site Concrete, Ramps, Stairs, and ADA Improvements	168,098	0	889	•		•	
Landscaping, Irrigation, and Play Field Improvements	0	428,608	0				
Fencing and Gates Upgrades	4,500	0	0				
Asphalt and Play Court Renovations	1,500	0	0				
Technology System Improvements	241,875	56,250	138,750	•			
Fire Alarm/Life Safety	156,250	0	0	•			
Exterior Lighting Efficiency Improvements	16,250	0	0	•			•
Exterior Power Distribution Energy Improvements	157,500	0	0				
Exterior Lighting Efficiency Improvements	82,500	0	0	•			•
Building Lighting Efficiency Improvements	42,500	0	0	•			•
Replace and/or repair roofing, roof fences and fascia	0	271,875	0				
Improve planter drainage	0	3,125	0				
Subtotals	\$ 929,804	\$ 759,858	\$ 297,139				
<b>Administration</b>							
Technology System Improvements	98,750	16,250	178,125	•			
ADA Required upgrades	0	14,175	0			•	
Building Power Distribution Energy Improvements	0	0	16,250				•
Classroom Plumbing Replacement	0	1,906	8,844			•	•
Repair and/or Replace casework	0	14,203	0			•	
Repair and/or replace floors and floor coverings	0	13,375	0		•		
Repair and/or replace window, door and hardware systems	0	9,391	0			•	
Toilet Room Plumbing Replacement.	0	2,859	16,516			•	•
Building Lighting Efficiency Improvements	0	0	22,500	•			•
Subtotals	\$ 98,750	\$ 72,159	\$ 242,234				



## Summary by Location, Priority and Special Categories

Century Elementary School	1-2	3-5	6-10	H&S	DFM	ADA	EE
<b>C-a, C-b, C-c, C-d, C-e</b>							
Building Lighting Efficiency Improvements	0	0	50,000	●			●
Building Power Distribution Energy Improvements	0	0	37,500				●
Repair and/or replace floors and floor coverings	0	279,813	0		●		
Repair and/or Replace casework	0	32,344	0			●	
ADA Required upgrades	0	3,375	0			●	
Technology System Improvements	211,250	0	68,750	●			
Classroom Plumbing Replacement	0	4,156	84,734			●	●
HVAC/Chiller Upgrade and/or Replacement	0	0	322,225	●			●
Replace and/or add Play Area or Athletic Field facilities	0	15,875	0				
Subtotals	\$ 211,250	\$ 335,563	\$ 563,209				
<b>Library Media Center</b>							
Repair and/or replace window, door and hardware systems	0	445	0			●	
Expand and/or reconfigure Library Media Center building	0	612,500	0				
Repair and/or Replace casework	0	7,969	0			●	
Repair and/or replace floors and floor coverings	0	51,094	0		●		
Repair and/or replace interior wall finishes	0	8,000	0				
ADA Required upgrades	0	3,375	0			●	
Subtotals	\$ 0	\$ 683,383	\$ 0				
<b>Multipurpose</b>							
Classroom Plumbing Replacement	2,125	953	15,344			●	●
Toilet Room Plumbing Replacement.	0	953	68,000			●	●
Expand and/or reconfigure Multipurpose building	0	265,563	0	●			
Repair and/or Replace casework	0	23,859	0			●	
Technology System Improvements	131,250	0	48,125	●			
Repair and/or replace floors and floor coverings	0	100,781	0		●		
Repair and/or replace interior wall finishes	0	8,000	0				
HVAC/Chiller Upgrade and/or Replacement	0	7,719	248,525	●			●
Building Power Distribution Energy Improvements	0	0	16,250				●
Building Lighting Efficiency Improvements	0	0	22,500	●			●
Repair and/or replace window, door and hardware systems	0	445	0			●	
Subtotals	\$ 133,375	\$ 408,273	\$ 418,744				



## Summary by Location, Priority and Special Categories

Century Elementary School	1-2	3-5	6-10	H&S	DFM	ADA	EE
<b>Portables</b>							
Classroom Plumbing Replacement	1,906	3,281	30,109			•	•
Repair and/or replace interior wall finishes	0	13,500	0				
Repair and/or replace window, door and hardware systems	0	4,250	0			•	
Repair and/or replace floors and floor coverings	0	51,094	0		•		
Technology System Improvements	42,250	0	13,750	•			
Building Power Distribution Energy Improvements	0	0	7,500				•
Repair and/or Replace casework	0	422	0			•	
Paint interior and/or exterior walls	0	27,000	0		•		
HVAC/Chiller Upgrade and/or Replacement	0	115,781	2,600	•			•
EMS Upgrade and/or Replacement	0	129,688	0				•
ADA Required upgrades	0	3,038	0			•	
Building Lighting Efficiency Improvements	0	0	10,000	•			•
Subtotals	\$ 44,156	\$ 348,053	\$ 63,959				
<b>Snack Bar</b>							
Toilet Room Plumbing Replacement	0	0	57,719			•	•
ADA Required upgrades	0	3,375	0			•	
Repair and/or Replace casework	0	844	0			•	
Repair and/or replace floors and floor coverings	0	44,531	0		•		
Classroom Plumbing Replacement	0	0	16,297			•	•
HVAC/Chiller Upgrade and/or Replacement	0	0	7,800	•			•
Subtotals	\$ 0	\$ 48,750	\$ 81,816				



HMC Architects • 1827 E. Fir Avenue, Suite 103, Fresno, CA 93720  
t. 559-322-2444, f. 559-322-2445, [www.hmcarchitects.com](http://www.hmcarchitects.com)



**HMC**  
Architects
